

PROPOSITION R
MONTHLY EXECUTIVE UPDATE

PROGRAM UPDATE

FEBRUARY 12, 2014

Field House Classroom Building


Accomplished in January

Continue rough utility work and interior framing

Planned for February

Interior drywall and finish utility work



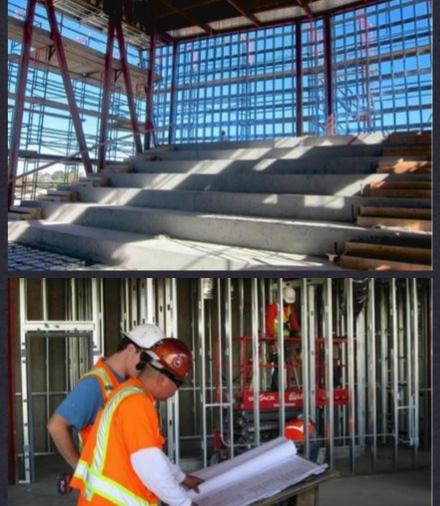



FIELD HOUSE BUILDING

CONCRETE FLOORS PLACED. UTILITY SYSTEMS AND INTERIOR FRAMING

Central Plant

Accomplished in January

 Received construction bids for system expansion

- Issue Notice to Proceed
 - Order materials
 - Late March 2014 construction



Solar Initiative Project

Accomplished in January

Executed design build contract

- Continue design work
- Lot surveys and soil sampling/testing


Emergency Communication System


Accomplished in January

* Continue system layout and design


- * Continue design
- * Summer 2014 installation



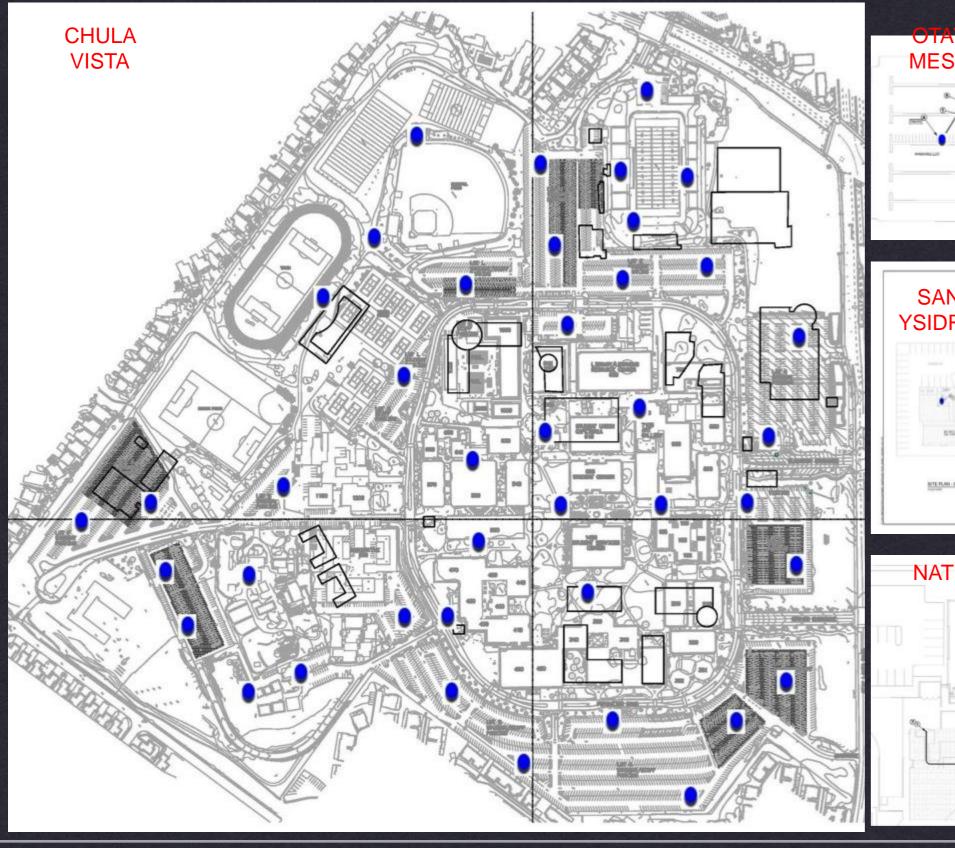





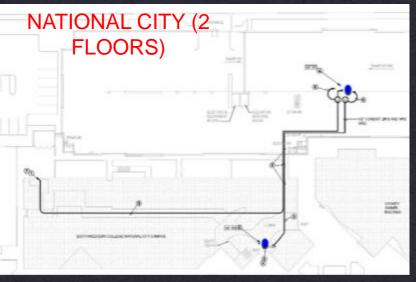

EMERGENCY COMMUNICATION SYSTEM LOCATIONS

CHULA VISTA CAMPUS AND HIGHER EDUCATION CENTERS

National City Phase II

Accomplished in January

- Programming complete
 - Program presentation to IFC

- Continue design
- Continue geo-technical work on the building site

Wellness Center


Accomplished in January

* Commenced project programing phase

- Complete programming
- * Start design phase

Other Initiatives

- Lot J entrance from H Street realignment
 - * February construction start
- * Sewer pump station
 - * March construction start
- Fire and potable water supply lines
 - * February construction bid advertisement
- Performing Arts and Cultural Center
 - Visit similar projects in February
 - Building User Group select architect short list

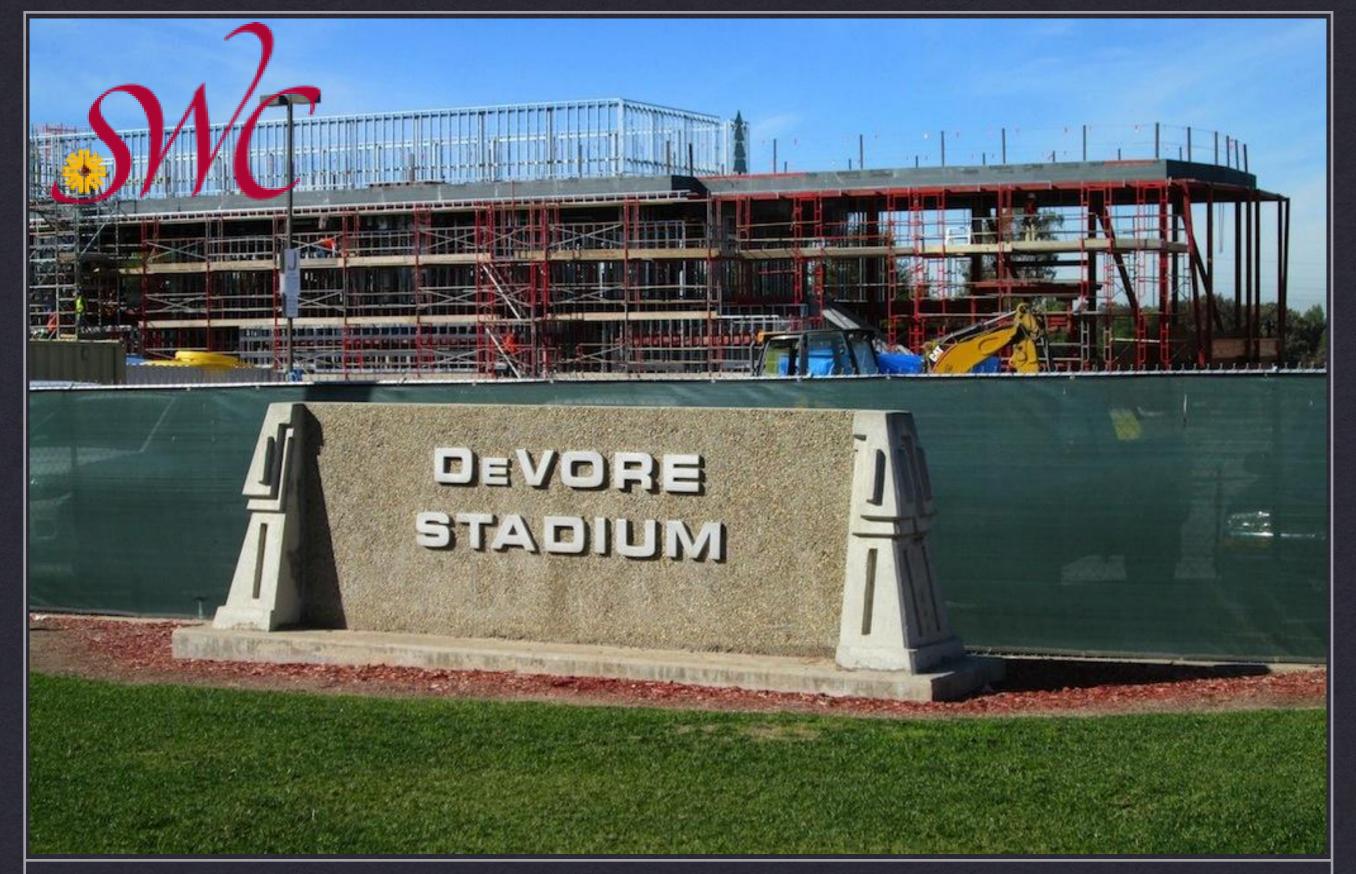

PROPOSITION R
MONTHLY EXECUTIVE UPDATE

PROJECT UPDATE

FEBRUARY 12, 2014
