

PROPOSITION R

MONTHLY EXECUTIVE UPDATE

PROGRAM UPDATE

**DECEMBER 11, 2013** 

# Field House Classroom Building

Accomplished in November

- Continued concrete floor pours and interior framing
- Completed structural steel erection
- Started rough utility work


Planned for December

- Complete concrete floors
- Continue rough utility work and interior framing



## FIELD HOUSE CLASSROOM BUILDING

Structural steel erection completed

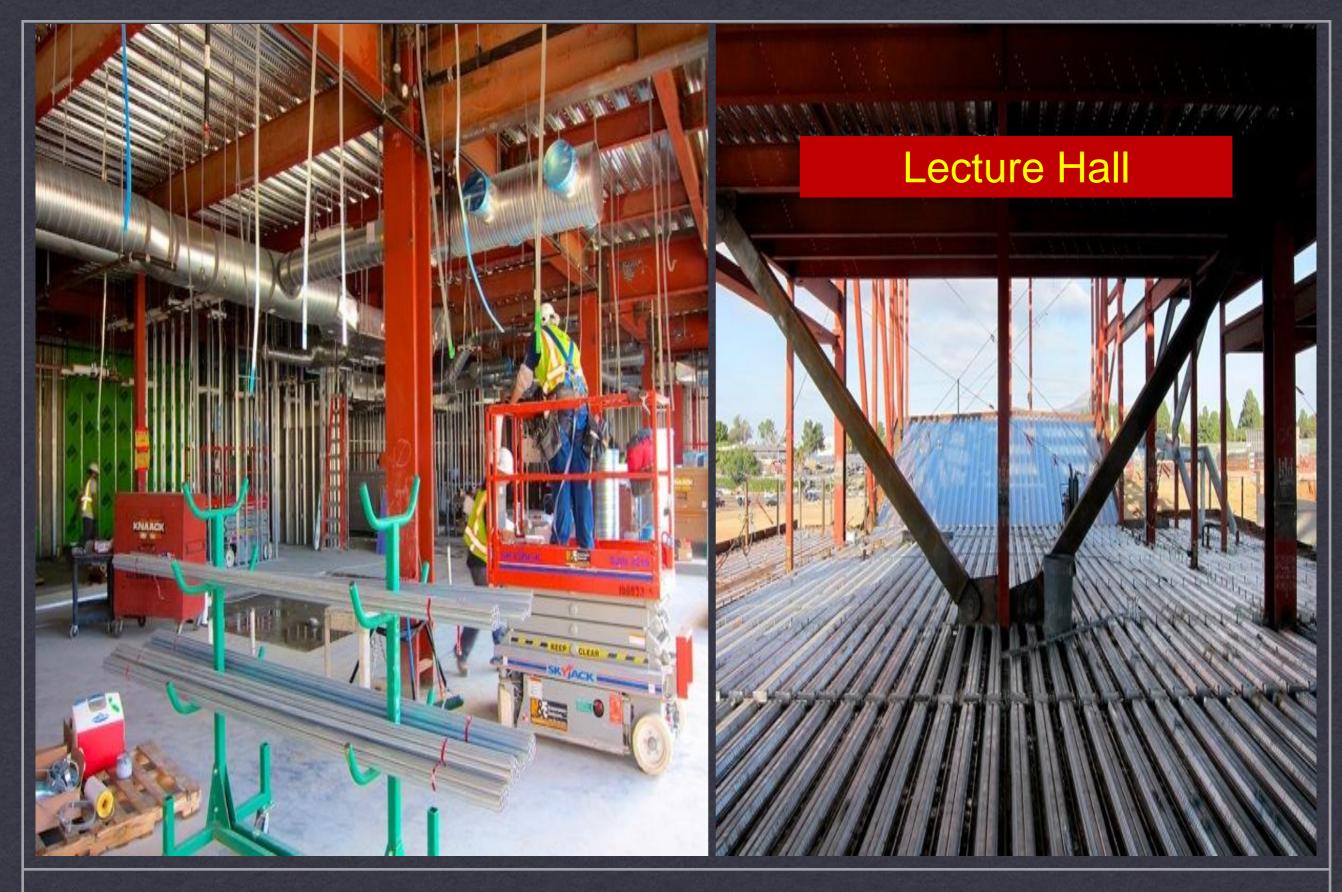

### FIELD HOUSE BUILDING INTERIOR

Rough utilities and interior room framing

# Solar Initiative Project

#### Accomplished in November

 Vendor selection and negotiation continuing

#### Planned for December

- Complete negotiations
- Prepare recommendation for Board review



Representation of Lot B

## Other Projects and Initiatives

#### Accomplished in November

- Received proposals from Architects for Wellness Center Project
- Reviewed Architect qualifications for Otay Mesa HEC Project with user group

#### Planned for December

- Release advertisement for contractors for Building exterior lock upgrades
- Select Architect for Otay Mesa HEC project
- Perform local college site visits for Math and Science Building project user group
- Complete Architect interviews for Wellness Center Project

## HEC National City Building II



**Building Program Presentation** 



PROPOSITION R

MONTHLY EXECUTIVE UPDATE

PROGRAM UPDATE

DECEMBER 11, 2013
