

PROPOSITION R
MONTHLY EXECUTIVE UPDATE

PROGRAM UPDATE

MARCH 12, 2014

Field House Classroom Building

Accomplished in February

* Continue interior framing, drywall and doors

Planned for March

Start interior finishes



FIELD HOUSE BUILDING

Framing Finishes and Exterior Doors

Central Plant Extension

Accomplished in February

- * Issued construction contract
- Ordering materials

Planned for March

Late March construction start



Solar Initiative Project

Accomplished in February

- Complete site surveys
- Continue design work

Planned for March

Continue design work

Emergency Communication System


Accomplished in February


* Completed design


Planned for March


* Design reviews



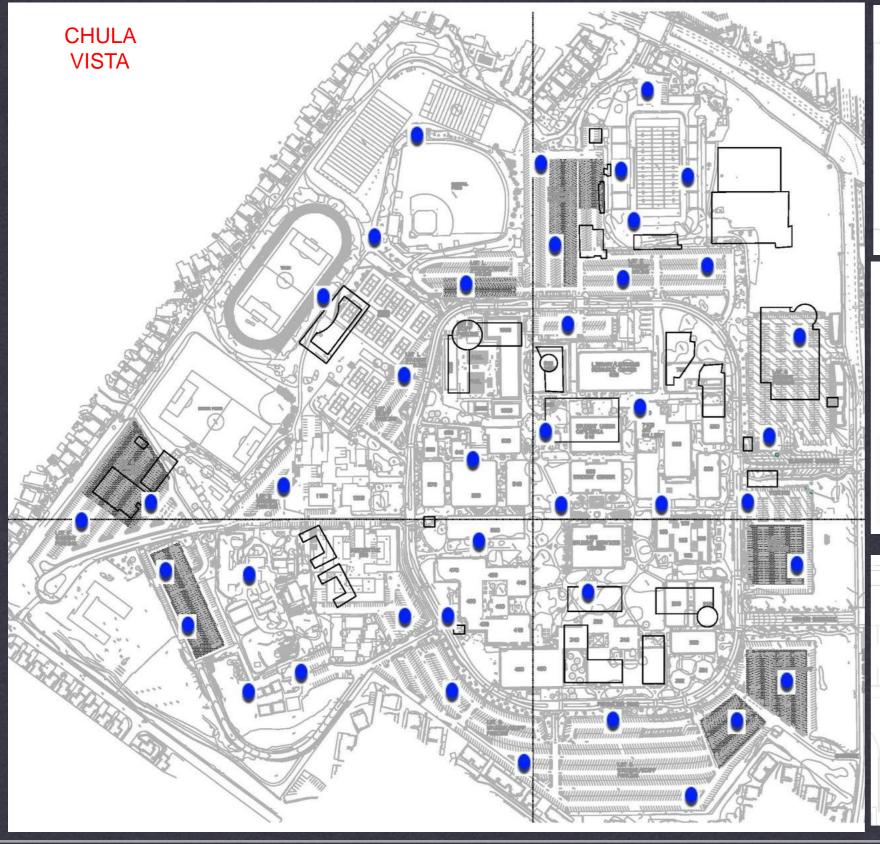



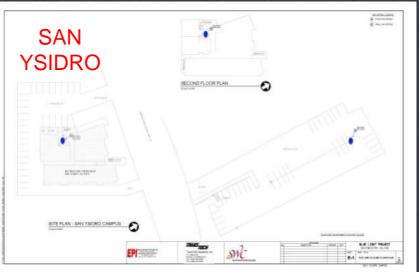

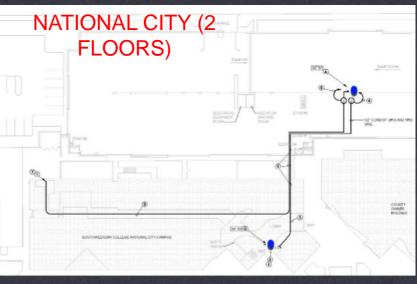

EMERGENCY COMMUNICATION SYSTEM

CHULA VISTA CAMPUS AND HIGHER EDUCATION CENTERS

National City Phase II

Accomplished in February

- * Schematic design complete for District review
- Geo-technical work complete

Planned for March

- Meetings with National City planning department
- Start environmental planning review (CEQA)

Wellness Center

Accomplished in February

- * Continuing programming phase
- * Weekly meetings with District and building user group

Planned for March

* Start schematic development

Math and Science

Accomplished in February

* Architect interviews

Planned for March

- * Board approval of recommended Architect
- * Start programming phase

Lot J Road Realignment

Accomplished in February

- * Construction start
- * Lot O expanded for interim parking

Planned for March

* Continue construction









LOT J ROAD REALIGNMENT

IMPROVE VEHICLE ACCESS ROAD AND PARKING FOR SOLAR PANEL PLACEMENT

Performing Arts

Accomplished in February

- * Visit similar projects
- Building user group developing architect short list for the proposal process from list of qualified architects

Planned for March

* Issue request for proposal





Other Initiatives

Chula Vista Campus infrastructure survey District Design Standards

- * Furniture and space layout
- Audio visual equipment
- Interior finishes

Fire and potable water line additions, Chula Vista campus

Small project Architect recommendation

Otay Mesa project

Classroom exterior lock upgrades





PROPOSITION R
MONTHLY EXECUTIVE UPDATE

PROJECT UPDATE

MARCH12, 2014
