SWCCD Major Projects Data Date November 28 2017 | DRAFT | 28-Nov-17 11:18

Activity Name	Start	Finish
National City HEC Classroom Building		
Construction	22-Mar-16 A	02-Jan-18
Commissioning, Furnish and Occupy	02-Jan-18	30-Jan-18
Wellness and Aquatics Complex		
Programming Phase	03-Feb-14 A	13-Aug-14 A
Increment 1 (Infrastructure) Design	14-Aug-14 A	01-May-15 A
Increment 1 (Infrastructure) DSA Approval	04-May-15 A	15-Jul-15 A
Increment 1 (Infrastructure) Construction	24-Nov-15 A	28-Jun-16 A
Wellness Center Design	14-Aug-14 A	22-Jul-15 A
Wellness Center Bidding Phase	11-Feb-16 A	30-Mar-16 A
Increment 1 (Infrastructure) Bidding Phase	16-Jul-15 A	25-Sep-15 A
Wellness Center DSA Approval	22-Jul-15 A	10-Feb-16 A
Wellness Center Construction	27-Apr-16 A	01-Dec-17
Commissioning, Furnish and Occupy	01-Dec-17	29-Dec-17
Math, Science and Engineering Building		
Design	01-May-14 A	01-Sep-15 A
DSA Approval	02-Sep-15 A	11-May-16 A
Bidding Phase	20-May-16 A	22-Aug-16 A
Construction	23-Jun-16 A	29-Oct-18
Commissioning, Furnish and Occupy	30-Oct-18	26-Nov-18
Performing Arts Curtural Center Complex		
Design	02-Mar-15 A	18-Nov-16 A
DSA Approval	16-Nov-16 A	14-Dec-17
Bidding Phase	26-Jan-18	10-May-18
Construction	11-May-18	15-Aug-19
Commissioning, Furnish and Occupy	16-Aug-19	07-Nov-19
IT; Security; Infrastructure		
Design and Construction	01-Jun-14 A	19-Feb-18
Security Complex		
Design	02-Mar-15 A	17-Nov-16 A
DSA Approval	18-Nov-16 A	09-Oct-17 A
Bidding Phase	22-Jan-18	16-Mar-18
Construction	19-Mar-18	08-Feb-19
Commissioning, Furnish and Occupy	11-Feb-19	12-Mar-19

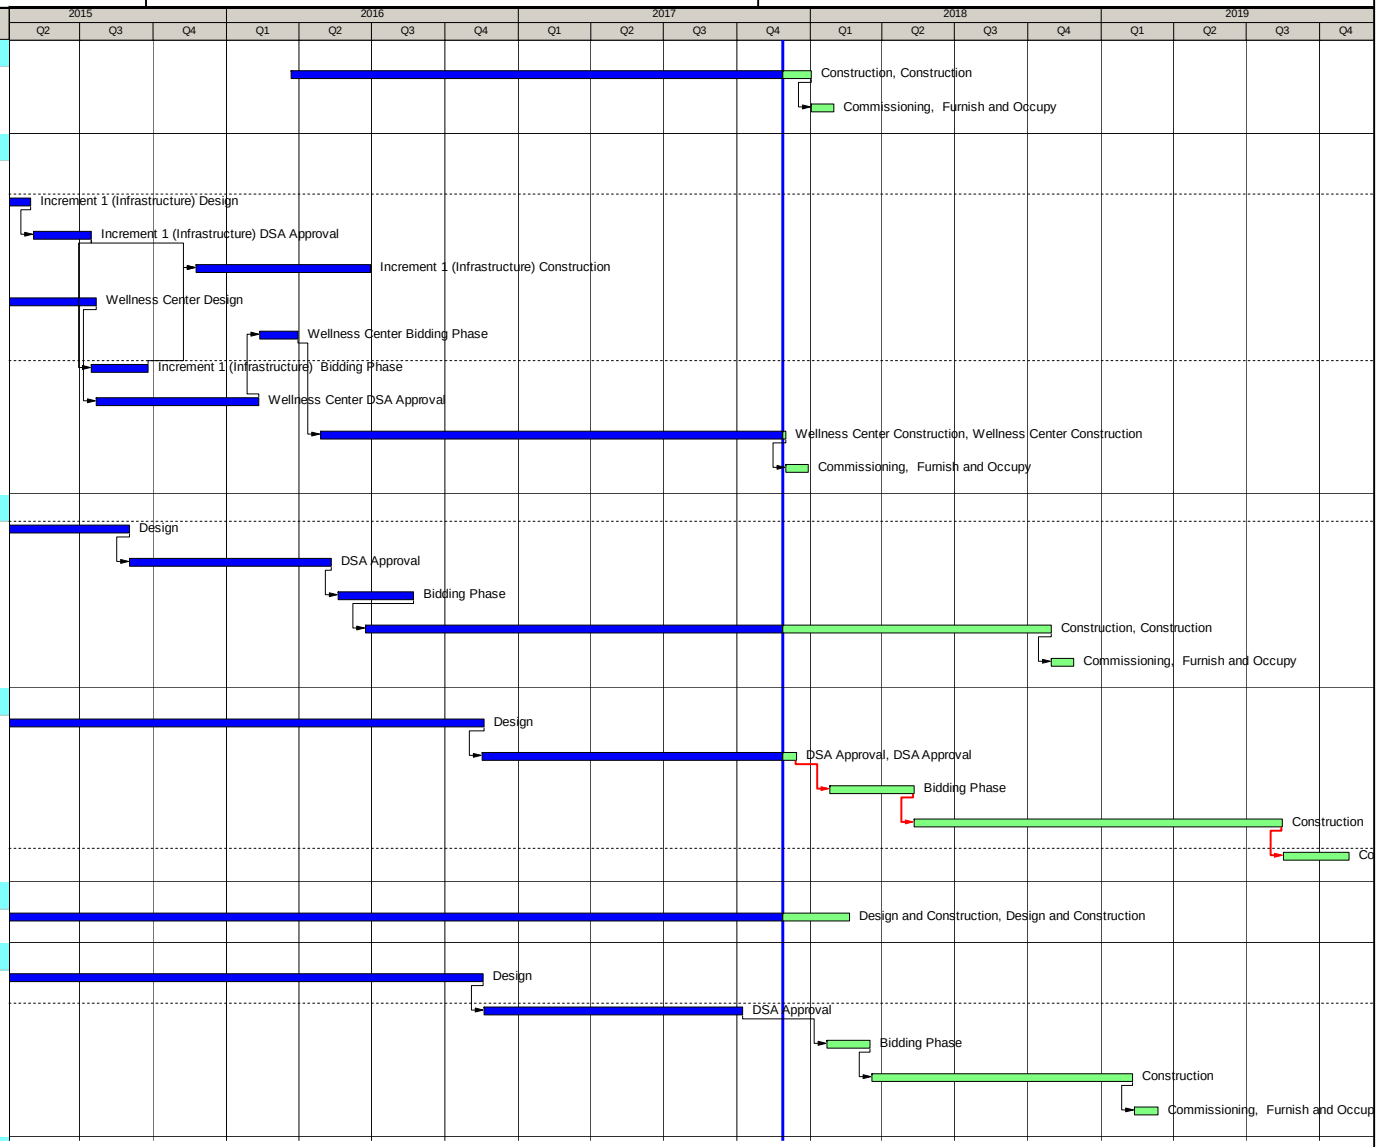

Actual Work | Critical Remaining ... | Remaining Work | ◆ Milestone
