

Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services



Audio-video

Scope of work with room requirements

Institutional Technology Department

9/28/2016

This document shows the specific details for each room that are being upgraded at Otay Mesa, National City and main campus in Chula Vista. Information includes the project coordinator, the room technician, a map of the room showing the orientation, the specific items being upgraded, notes about the room, and the room availability.

Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Contents

Introduction	3
Room 301, MSE.....	4
Room 302, MSE.....	5
Room 411A, Language Arts & Literature	6
Room 411B, Language Arts & Literature (changed 411A to 411B).....	7
Room 412, Language Arts & Literature.....	8
Room 413, Language Arts & Literature.....	9
Room 414, Language Arts & Literature.....	10
Room 415, Language Arts & Literature.....	11
Room 416, Language Arts & Literature.....	12
Room 417, Language Arts & Literature.....	13
Room 418, Language Arts & Literature.....	14
Room 422, Language Arts & Literature.....	15
Room 423, Language Arts & Literature.....	16
Room 427, Language Arts & Literature.....	17
Room 428, Language Arts & Literature.....	18
Room 429, Language Arts & Literature.....	19
Room 431, Language Arts & Literature.....	20
Room 433, Language Arts & Literature.....	21
Room 441, Language Arts & Literature.....	22
Room 442, Language Arts & Literature.....	23
Room 443, Language Arts & Literature.....	24
Room 444, Language Arts & Literature.....	25
Room 445, Language Arts & Literature.....	26
Room 447, Language Arts & Literature.....	27
Room 551, Language Arts & Literature.....	28
Room 551A, Language Arts & Literature	29
Room 555, Language Arts & Literature.....	30
Room 562, Language Arts & Literature.....	31
Room 563A, Language Arts & Literature	32
Room 652, Office of Instruction.....	33

Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 564B, Language Arts & Literature	35
Room 705, Language Arts & Literature.....	36
Room 4500, Otay Mesa.....	38
Room 7120, National City Library	39
Room 7202, National City	40
Room 7203, National City	41
Room 7205, National City	42
Room 7206, National City	43
Room 7208A, National City	45
Room 7208B, National City	46
Room 7210, National City	48
Room 7211, National City	49
Room 7212, National City	50
Room 7213, National City	51
Room 7214, National City	52
Room 7215, National City	53
Room 7216, National City	54

Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Introduction

Southwestern College seeks a contractor to provide the labor and services required to upgrade and integrate audiovisual systems into several areas of Southwestern College. The goal of this project is to provide cutting edge technology to faculty to improve the classroom experience for students. The two primary areas include the School of Language, Literature, and Humanities on the Chula Vista campus and the Higher Education Center at National City. The purpose of this project is to update antiquated technology that is in some cases over 10 years old. The following table indicates the number of rooms and the departments where they are located:


Location	Number
Chula Vista	32
HEC, National City	14
HEC, Otay Mesa	1
Total	47

This project will required a significant coordination effort between the vendor with the awarded contract, the Institutional Technology (IT) department, and each campus listed above where the objective is to not impact scheduled classes. In some cases, simple equipment replacement will be required and in others, a complete integration of new Audiovisual (AV) equipment will be necessary. The scheduled bid walk on 10/14/16 will be used to show the requirement in each room.

The overall design and the specific equipment that will be used has been documented in the Southwestern Design for Smart Classrooms. This document was created as a joint effort between the IT department and Instruction and is a culmination of planned technology strategies that will be employed at Southwestern College as technology moves into the 21st century.

Although more specific details are available from the Southwestern AV equipment list, the basic replacement equipment includes an AV Lectern with both sit and stand surfaces. An Extron room controller with a matrix switcher will be connected to either an HP mini or all-in-one computer connected by HDMI to a Casio lamp-less 3000 lumen projector. Other features include spare connections for guest devices, Blu-ray player, room speakers, and optional equipment such as document cameras, assisted listening, and microphone systems. All of this equipment is designed to fit into a standard AV rack that is then mounted and installed into the AV lectern in the space underneath the standing side of the podium. Additional details for each room are provided in the rest of this document.

Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services
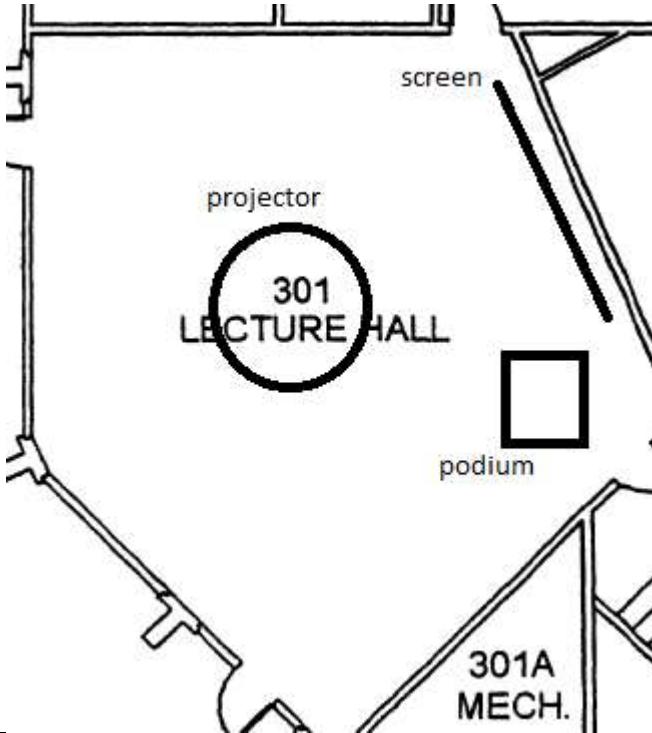
<p>Room 301, MSE</p> <p>Project Coordinator: Hector Reyes</p> <p>Instructional Lab Technician: Genaro Ornelas</p> <p>Room Layout (from room inventory document)</p>

<p>Upgrade components:</p> <ul style="list-style-type: none">KI podiumA/V rackHP AIOTCL pro 720 touch panelProjector ScreenCeiling speakers - time twoBlu-rayMicrophone/ assisted listeningDoc camConfidence monitor
<p>Notes:</p> <p>Projector Replaced</p> <p>Room Availability: M-Th 8AM-7PM End 8/4/2016</p>

Appendix I: Task Order 1- AV Room Scope

RFP No. 1617 -151 Professional Audio-Visual Design,


Integration/Implementation Services

Room 302, MSE

Project Coordinator: **Hector Reyes**

Instructional Lab Technician: **Genaro Ornelas**

Room Layout (from room inventory document)

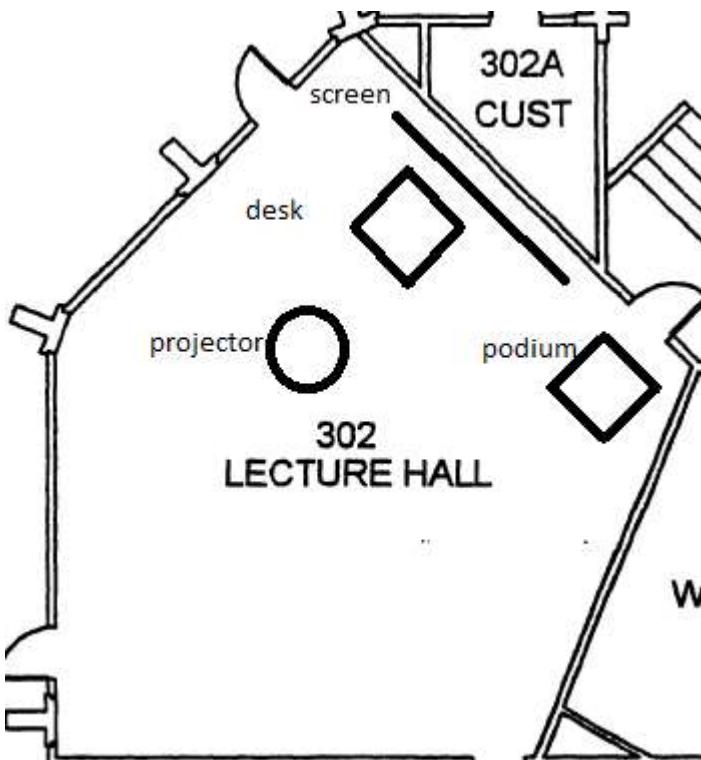

Upgrade components:

KI podium

A/V rack

HP AIO

TCL pro 720 touch panel

Projector Screen

Ceiling speakers - time two

Blu-ray

Microphone/ assisted listening

Doc cam

Confidence monitor

Notes:

Projector Replaced

Room Availability:

M-Th 5:30AM-8:30PM End 8/4/2016


Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 411A, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Barry Thele**

Room Layout (from room inventory document)

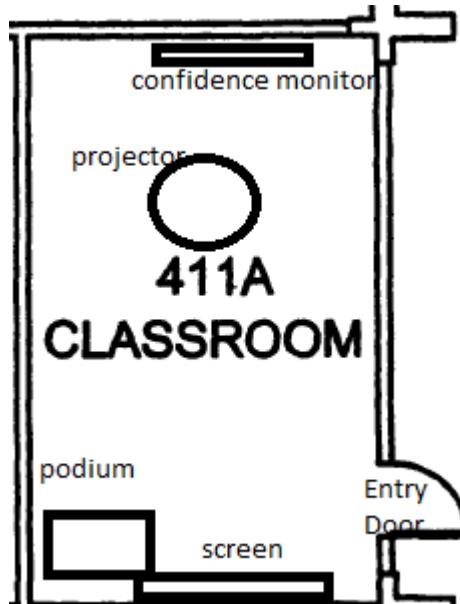

Upgrade components:

Use existing podium retro -fit

A/V rack

HP Mini

TLP PRO 520M

Cable Cubby 1200

Projector Screen

Ceiling speakers

Blu-ray

Confidence monitor

Notes:

Projector Replaced

Room Availability:

M-Th 10:30AM-11:30AM End 8/4/2016

Appendix I: Task Order 1- AV Room Scope

RFP No. 1617 -151 Professional Audio-Visual Design,


Integration/Implementation Services

Room 411B, Language Arts & Literature (changed 411A to 411B)

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Barry Thele**

Room Layout (from room inventory document)

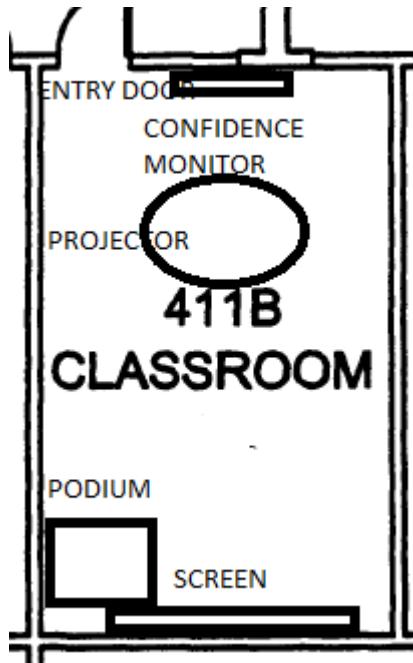

Upgrade components:

Use existing podium retro -fit

A/V rack

HP Mini

TLP PRO 520M

Cable Cubby 1200

Projector Screen

Ceiling speakers

Blu-ray

Confidence monitor

Notes:

Projector Replaced

Room Availability: Available all summer

Appendix I: Task Order 1- AV Room Scope

RFP No. 1617 -151 Professional Audio-Visual Design,


Integration/Implementation Services

Room 412, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Barry Thele**

Room Layout (from room inventory document)

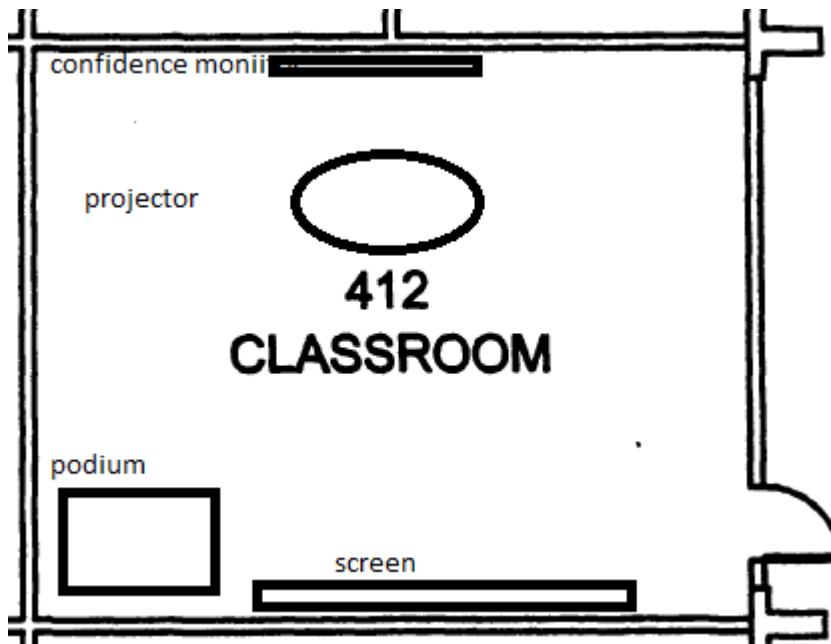

Upgrade components:

- KI podium
- A/V rack
- HP AIO
- TCL pro 720 touch panel
- Casio projector
- Projector Screen
- Ceiling speakers
- Blu-ray
- Microphone/ assisted listening
- Doc cam
- Confidence monitor

Notes:

Room Availability:

M-Th 8am-6pm

End 8/4/2016

Appendix I: Task Order 1- AV Room Scope

RFP No. 1617 -151 Professional Audio-Visual Design,


Integration/Implementation Services

Room 413, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Barry Thele**

Room Layout (from room inventory document)

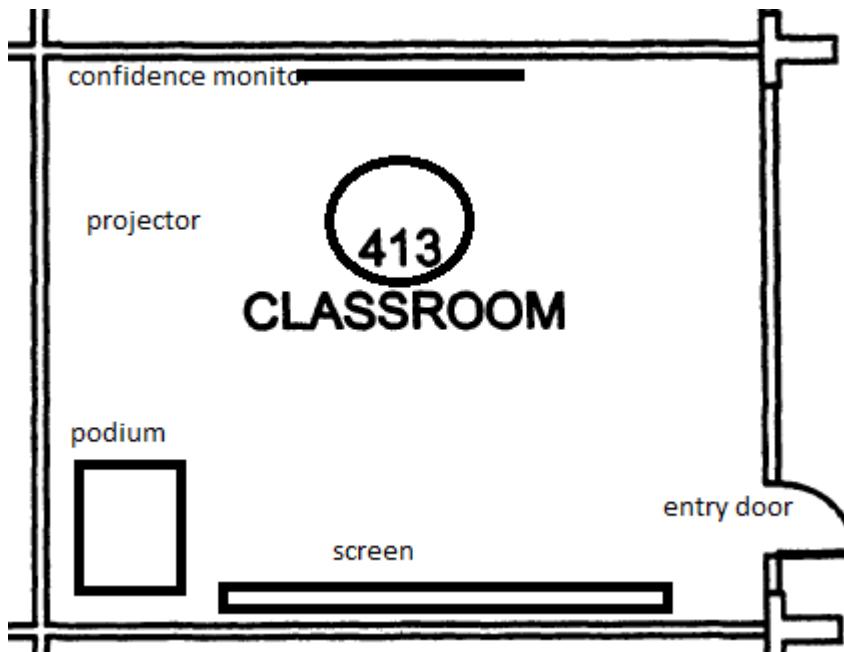

Upgrade components:

KI podium
A/V rack
HP AIO
TCL pro 720 touch panel
Projector Screen
Ceiling speakers
Blu-ray
Microphone/ assisted listening
Doc cam
Confidence monitor

Notes:

Projector Replaced

Room Availability:

M-Th 8am-8pm

8/4/2016

Appendix I: Task Order 1- AV Room Scope

RFP No. 1617 -151 Professional Audio-Visual Design,


Integration/Implementation Services

Room 414, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Barry Thele**

Room Layout (from room inventory document)

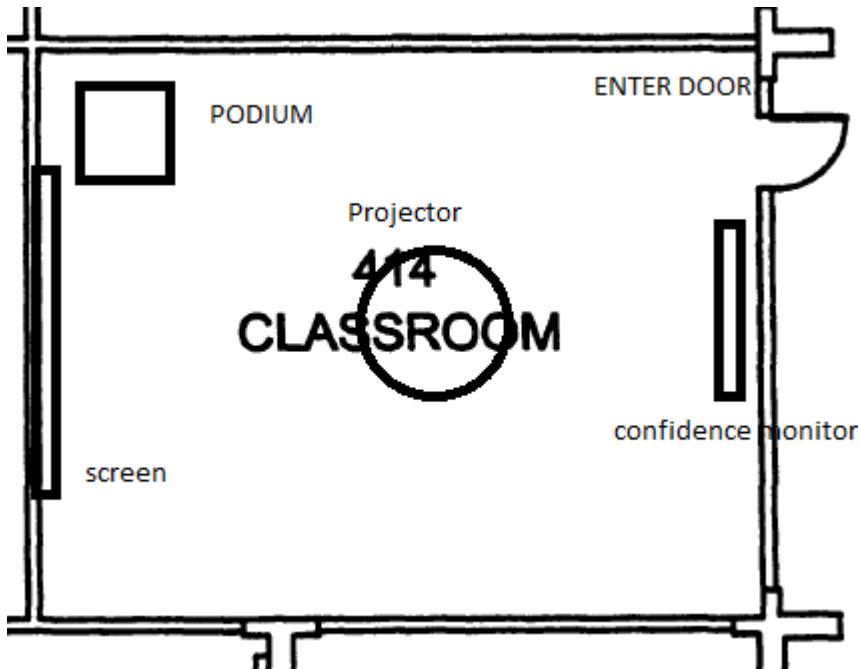

Upgrade components:

KI podium
A/V rack
HP AIO
TCL pro 720 touch panel
Projector Screen
Ceiling speakers
Blu-ray
Microphone/ assisted listening
Doc cam
Confidence monitor

Notes:

Projector Replaced

Room Availability:

M-Th 8am-8pm End 8/4/2016

Appendix I: Task Order 1- AV Room Scope

RFP No. 1617 -151 Professional Audio-Visual Design,


Integration/Implementation Services

Room 415, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Barry Thele**

Room Layout (from room inventory document)

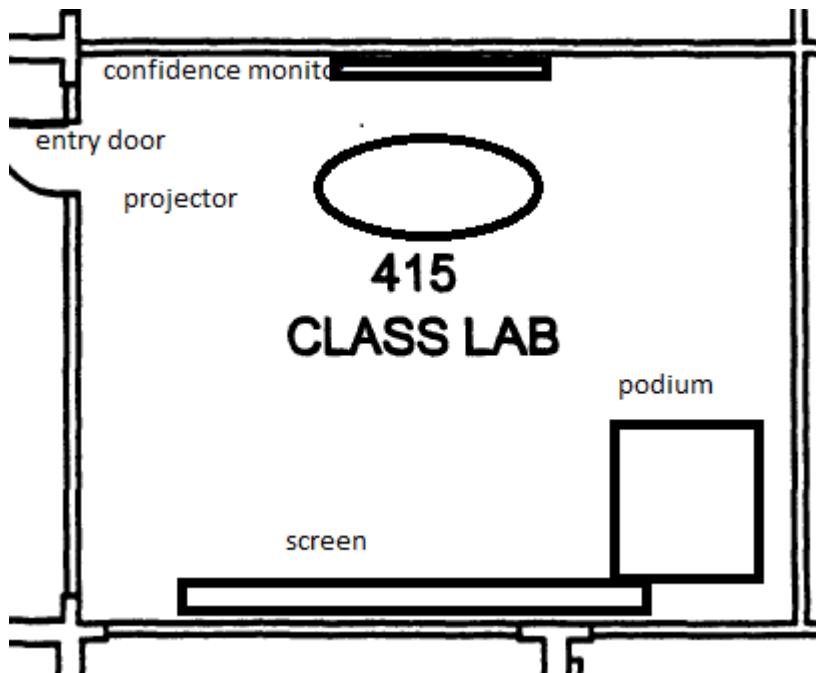

Upgrade components:

- KI podium
- A/V rack
- HP AIO
- TCL pro 720 touch panel
- Casio projector
- Projector Screen
- Ceiling speakers
- Blu-ray
- Microphone/ assisted listening
- Doc cam
- Confidence monitor

Notes:

Room Availability:

M-Th 8am-8:30PM

End 8/4/2016


Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 416, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Barry Thele**

Room Layout (from room inventory document)

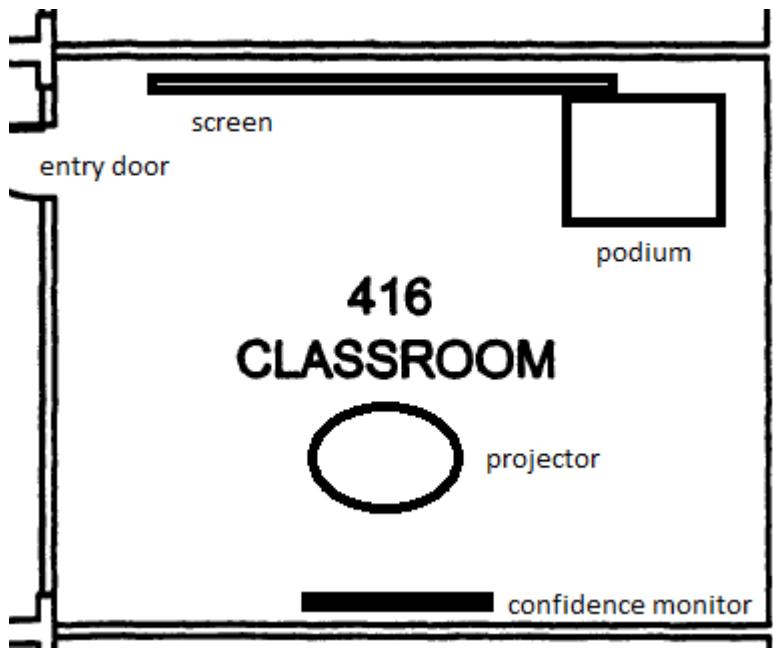

Upgrade components:

KI podium

A/V rack

HP AIO

TCL pro 720 touch panel

Projector Screen

Ceiling speakers

Blu-ray

Microphone/ assisted listening

Doc cam

Confidence monitor

Notes:

Projector Replaced

Room Availability:

M-Th 8am-8:30PM

End 8/4/2016


Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 417, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Barry Thele**

Room Layout (from room inventory document)

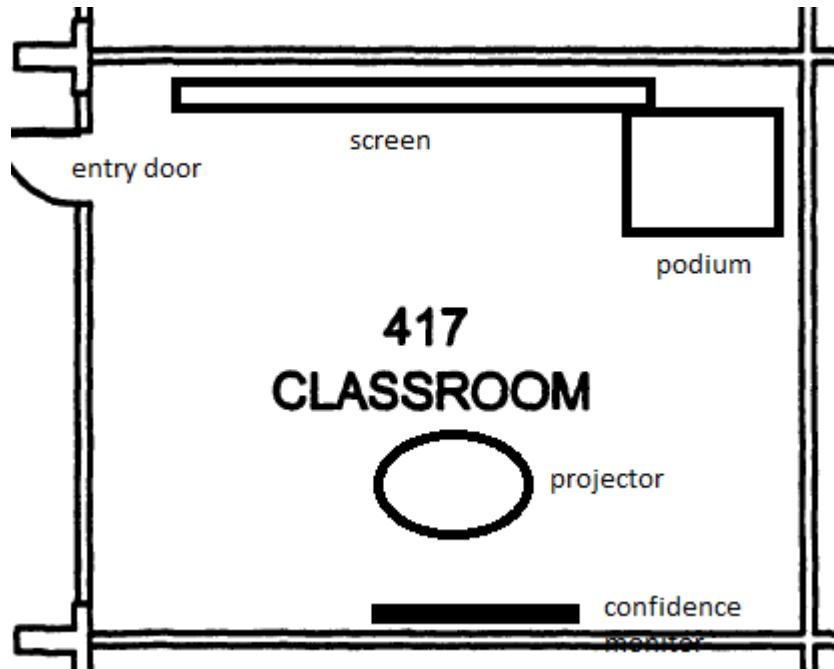

Upgrade components:

KI podium
A/V rack
HP AIO
TCL pro 720 touch panel
Projector Screen
Ceiling speakers
Blu-ray
Microphone/ assisted listening
Doc cam
Confidence monitor

Notes:

Projector Replaced

Room Availability:

M-Th 8am-1:00PM End 8/4/2016


Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 418, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Barry Thele**

Room Layout (from room inventory document)

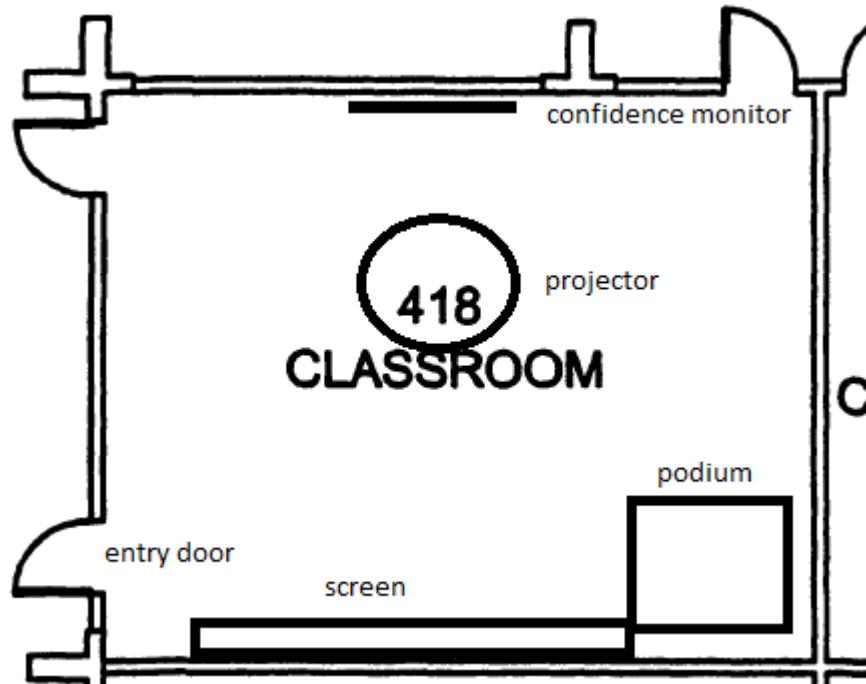

Upgrade components:

KI podium

A/V rack

HP AIO

TCL pro 720 touch panel

Projector Screen

Ceiling speakers

Blu-ray

Microphone/ assisted listening

Doc cam

Confidence monitor

Notes:

Projector Replaced

Room Availability:

M-Th 8am-1:00PM

End 8/4/2016

Appendix I: Task Order 1- AV Room Scope

RFP No. 1617 -151 Professional Audio-Visual Design,


Integration/Implementation Services

Room 422, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Genaro Ornelas**

Room Layout (from room inventory document)

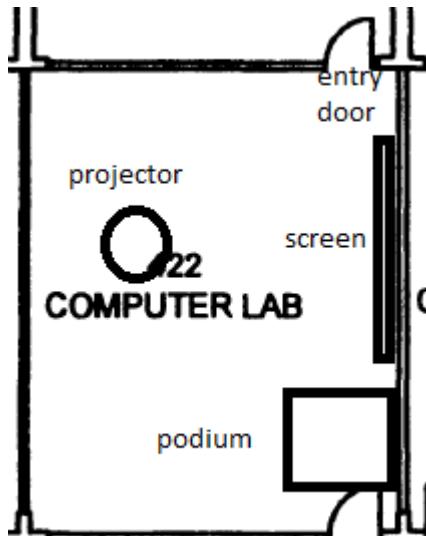

Upgrade components:

Use existing podium retro -fit

A/V rack

HP Mini

TLP PRO 520M

Cable Cubby 1200

Projector Screen

Ceiling speakers

Blu-ray

Microphone/ assisted listening

Notes:

Projector Replaced

Room Availability:

M-Th 7:30AM-1:00PM

End 8/4/2016


Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 423, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Genaro Ornelas**

Room Layout (from room inventory document)

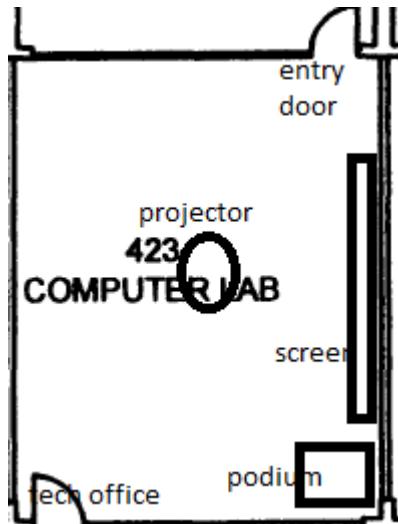

Upgrade components:

Use existing podium retro -fit

A/V rack

HP Mini

TLP PRO 520M

Cable Cubby 1200

Projector Screen

Ceiling speakers

Blu-ray

Microphone/ assisted listening

Notes:

Projector Replaced

Room Availability:

M-Th 7:30AM-8:00PM End 8/4/2016

Appendix I: Task Order 1- AV Room Scope


RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 427, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Barry Thele**

Room Layout (from room inventory document)

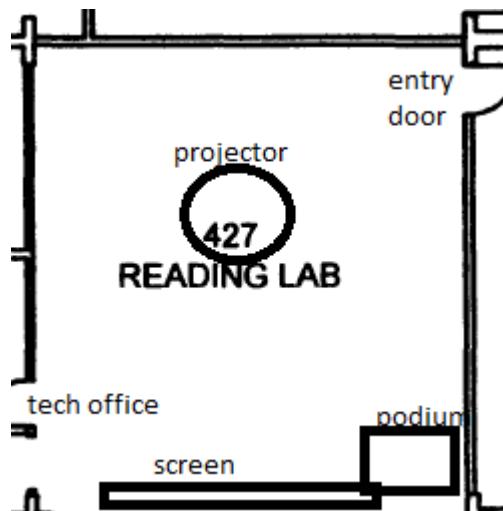

Upgrade components:

KI podium

A/V rack

HP AIO

TCL pro 720 touch panel

Projector Screen

Ceiling speakers

Blu-ray

Doc cam

Notes:

Projector Replaced

Room Availability:

M-Th 7:30AM-1:00PM End 7/28/2016


Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 428, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Barry Thele**

Room Layout (from room inventory document)

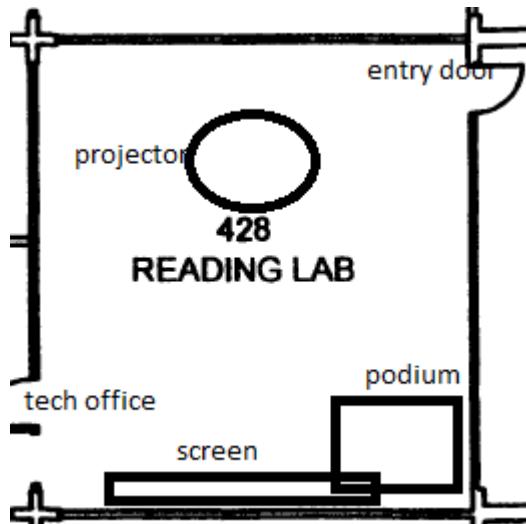

Upgrade components:

KI podium
A/V rack
HP AIO
TCL pro 720 touch panel
Projector Screen
Ceiling speakers
Blu-ray
Doc cam

Notes:

Projector Replaced

Room Availability:

M-Th 10:30AM-1:00PM End 7/21/2016

Appendix I: Task Order 1- AV Room Scope


RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 429, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Barry Thele**

Room Layout (from room inventory document)

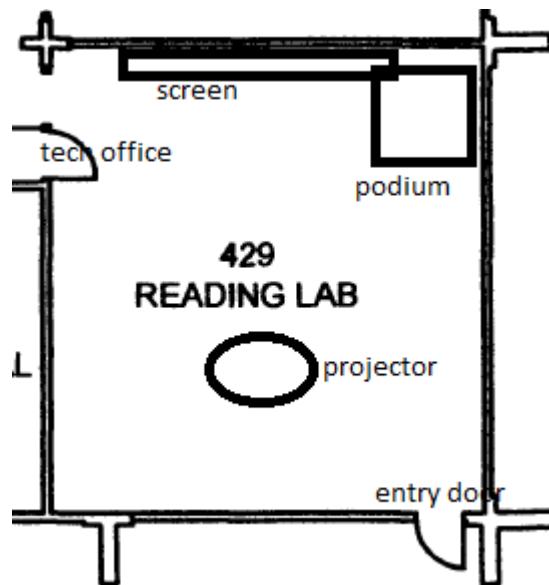

Upgrade components:

KI podium
A/V rack
HP AIO
TCL pro 720 touch panel
Projector Screen
Ceiling speakers
Blu-ray
Doc cam

Notes:

Projector Replaced

Room Availability:

M-W 8AM-8:15PM Th 8-1 End 7/21/2016

Appendix I: Task Order 1- AV Room Scope

RFP No. 1617 -151 Professional Audio-Visual Design,


Integration/Implementation Services

Room 431, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Barry Thele**

Room Layout (from room inventory document)

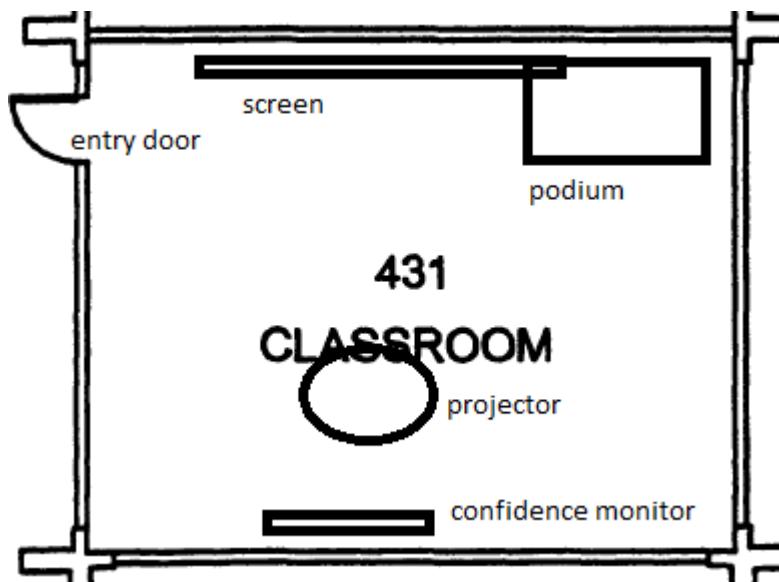

Upgrade components:

KI podium
A/V rack
HP AIO
TCL pro 720 touch panel
Projector Screen
Ceiling speakers
Blu-ray
Microphone/ assisted listening
Doc cam
Confidence monitor

Notes: has an audio receiver

Projector Replaced

Room Availability:

M-Th 8am-12:30PM

End 8/4/2016


Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 433, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Barry Thele**

Room Layout (from room inventory document)

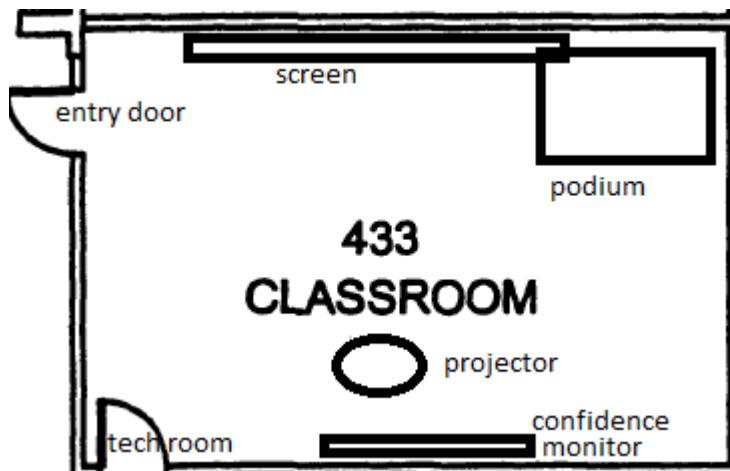

Upgrade components:

KI podium

A/V rack

HP AIO

TCL pro 720 touch panel

Projector Screen

Ceiling speakers

Blu-ray

Microphone/ assisted listening

Doc cam

Confidence monitor

Notes:

Projector Replaced

Room Availability:

M-Th 8AM-9:15PM

End 8/4/2016

Appendix I: Task Order 1- AV Room Scope

RFP No. 1617 -151 Professional Audio-Visual Design,


Integration/Implementation Services

Room 441, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Barry Thele**

Room Layout (from room inventory document)

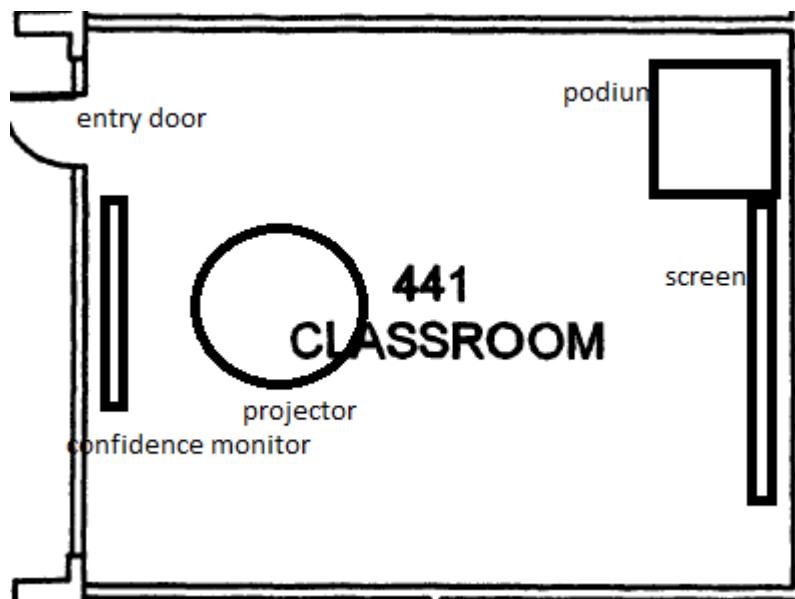

Upgrade components:

- KI podium
- A/V rack
- HP AIO
- TCL pro 720 touch panel
- Projector Screen
- Ceiling speakers
- Blu-ray
- Microphone/ assisted listening
- Doc cam
- Confidence monitor

Notes:

Projector Replaced

Room Availability:

M-Th 8AM-8:15PM

End 8/4/2016

Appendix I: Task Order 1- AV Room Scope


RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 442, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Barry Thele**

Room Layout (from room inventory document)

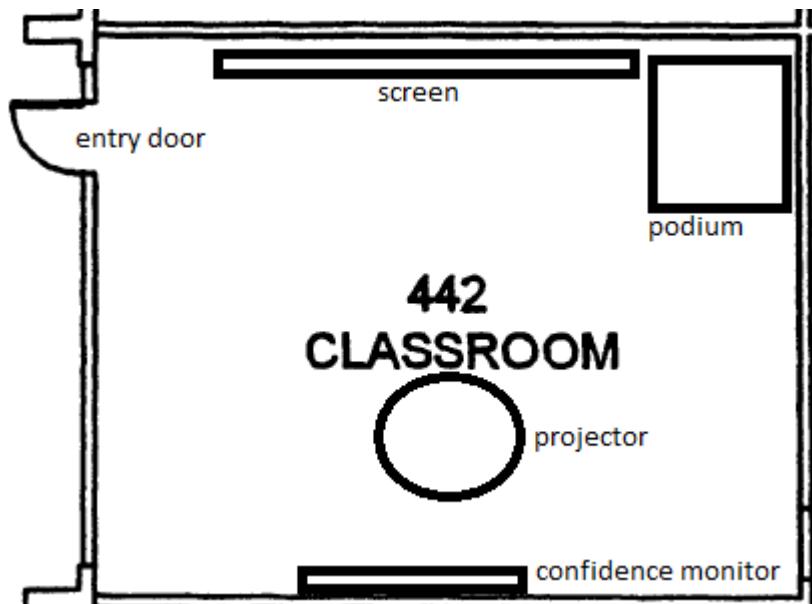

Upgrade components:

KI podium

A/V rack

HP AIO

TCL pro 720 touch panel

Casio projector

Projector Screen

Ceiling speakers

Blu-ray

Microphone/ assisted listening

Doc cam

Confidence monitor

Notes:

Room Availability:

M-Th 8AM-8:15PM

End 8/4/2016

Appendix I: Task Order 1- AV Room Scope

RFP No. 1617 -151 Professional Audio-Visual Design,


Integration/Implementation Services

Room 443, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Barry Thele**

Room Layout (from room inventory document)

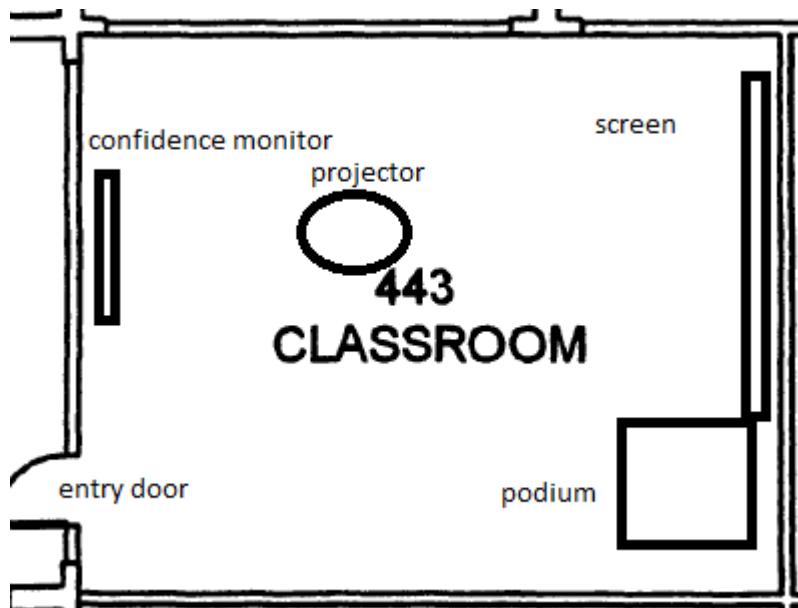

Upgrade components:

KI podium

A/V rack

HP AIO

TCL pro 720 touch panel

Projector Screen

Ceiling speakers

Blu-ray

Microphone/ assisted listening

Doc cam

Confidence monitor

Notes:

Projector Replaced

Room Availability:

M-Th 8:30AM-10:30AM End 8/4/2016

Appendix I: Task Order 1- AV Room Scope


RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 444, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Barry Thele**

Room Layout (from room inventory document)

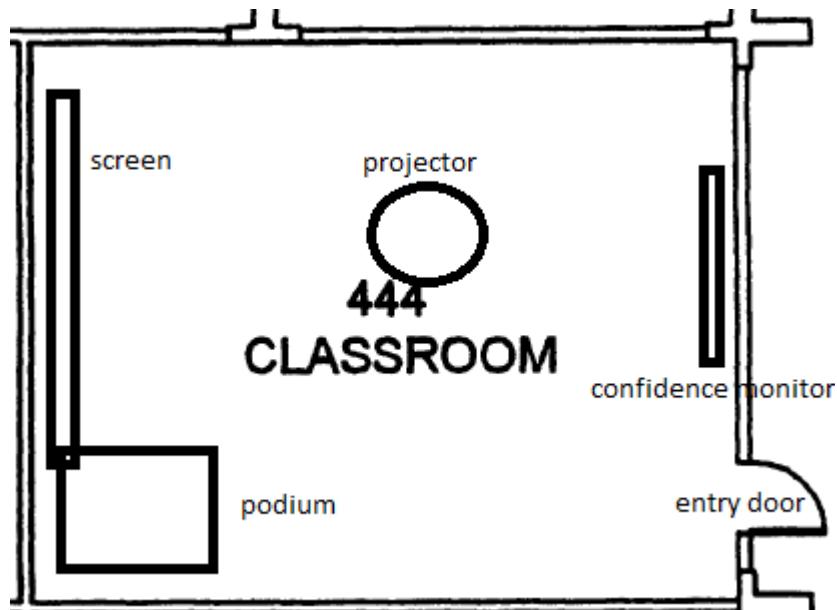

Upgrade components:

KI podium

A/V rack

HP AIO

TCL pro 720 touch panel

Projector Screen

Ceiling speakers

Blu-ray

Microphone/ assisted listening

Doc cam

Confidence monitor

Notes:

Projector Replaced

Room Availability:

M-Th 8:30AM-10:30AM End 8/4/2016


Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 445, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Junior**

Room Layout (from room inventory document)

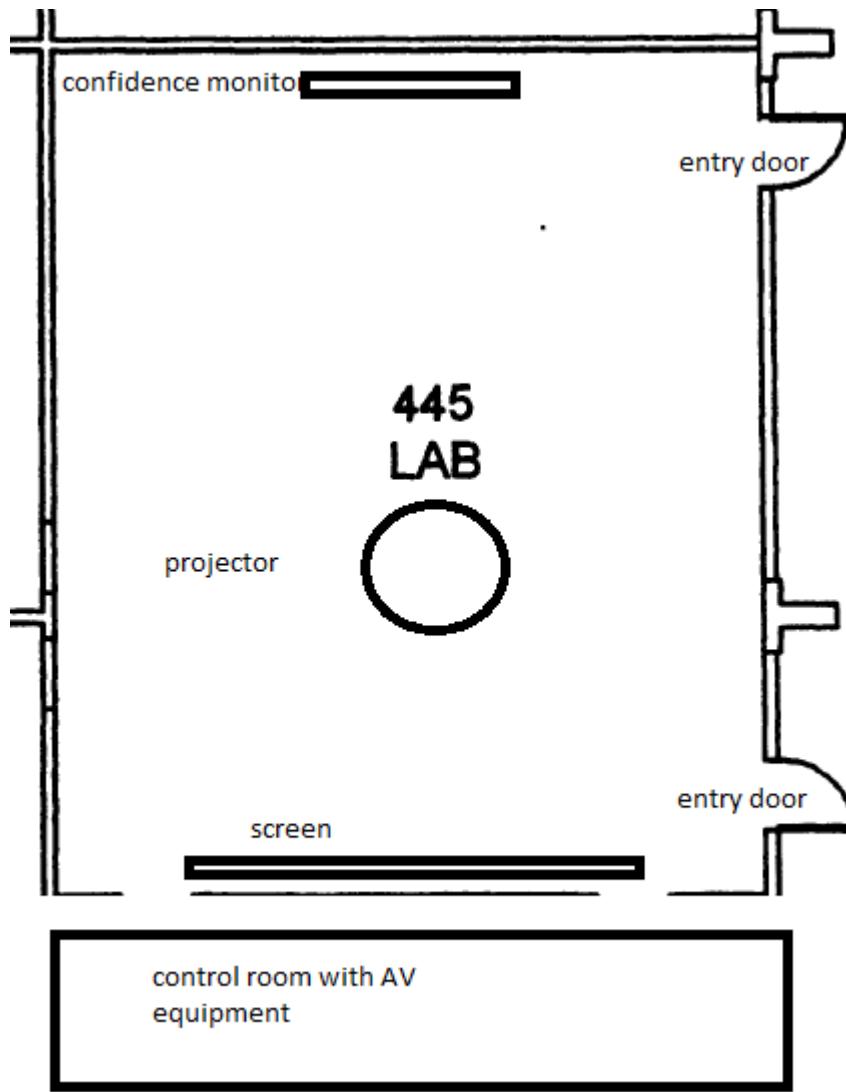

A/V rack

TLP PRO 520M

Projector Screen

Ceiling speakers - times two

Blu-ray

Microphone/ assisted listening

Confidence monitor

Notes: currently motorized screen

Projector Replaced

Appendix I: Task Order 1- AV Room Scope

RFP No. 1617 -151 Professional Audio-Visual Design,

Integration/Implementation Services


Room Availability: Available

Room 447, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Barry Thele**

Room Layout (from room inventory document)

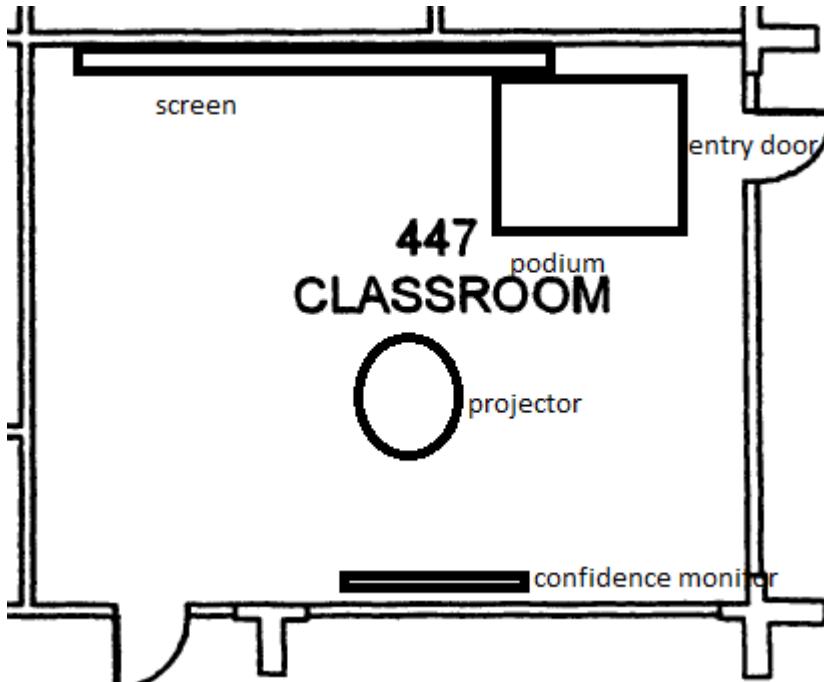

Upgrade components:

KI podium

A/V rack

HP AIO

TCL pro 720 touch panel

Casio projector

Projector Screen

Ceiling speakers

Blu-ray

Microphone/ assisted listening

Doc cam

Confidence monitor

Notes:

Room Availability:

M-Th 8AM-8:15PM

End 8/4/2016

Appendix I: Task Order 1- AV Room Scope

RFP No. 1617 -151 Professional Audio-Visual Design,


Integration/Implementation Services

Room 551, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Junior**

Room Layout (from room inventory document)

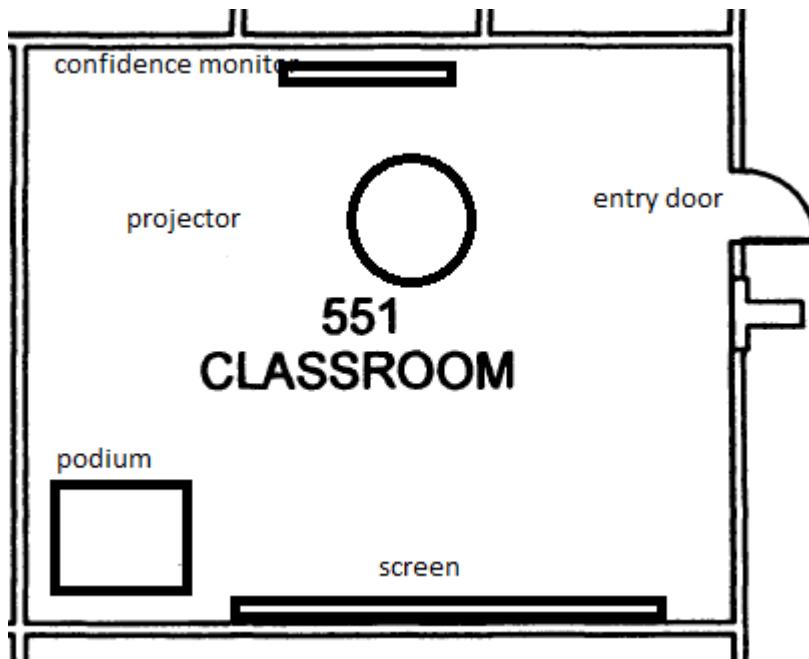

Upgrade components:

KI podium
A/V rack
HP AIO
TCL pro 720 touch panel
Projector Screen
Ceiling speakers
Blu-ray

Microphone/ assisted listening
Doc cam
Confidence monitor

Notes:

Projector Replaced

Room Availability:

M-Th 8:30AM-10:30AM End 8/4/2016


Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 551A, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Junior**

Room Layout (from room inventory document)

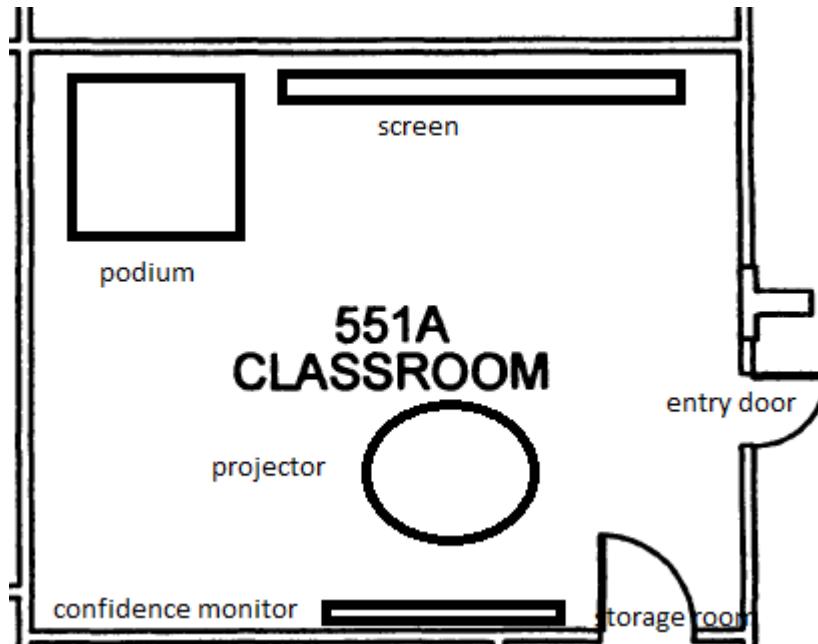

Upgrade components:

KI podium

A/V rack

HP AIO

TCL pro 720 touch panel

Projector Screen

Ceiling speakers

Blu-ray

Microphone/ assisted listening

Doc cam

Confidence monitor

Notes:

Projector Replaced

Room Availability: Available all summer


Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 555, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Junior**

Room Layout (from room inventory document)

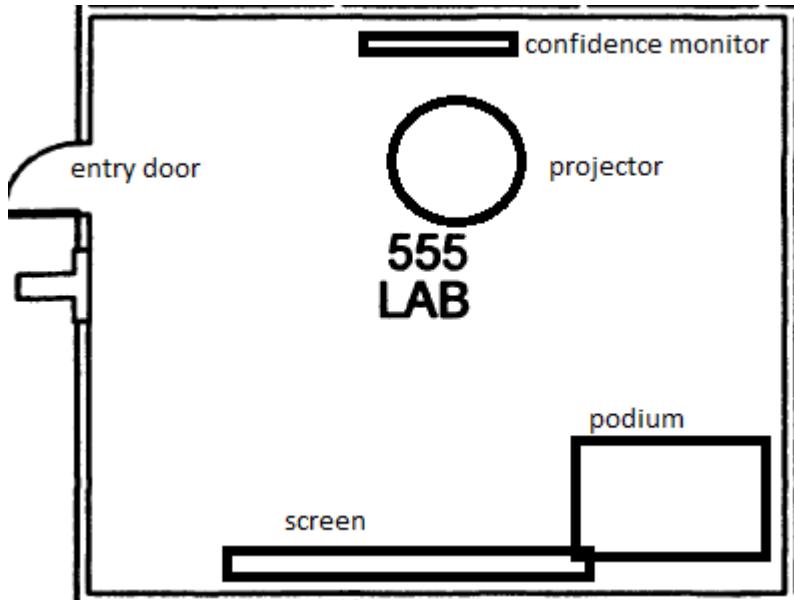

Upgrade components:

KI podium

A/V rack

HP AIO

TCL pro 720 touch panel

Projector Screen

Ceiling speakers

Blu-ray

Microphone/ assisted listening

Doc cam

Confidence monitor

Notes:

Projector Replaced

Room Availability:

M-Th 8AM-5:30PM

End 8/4/2016

Appendix I: Task Order 1- AV Room Scope


RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 562, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Junior**

Room Layout (from room inventory document)

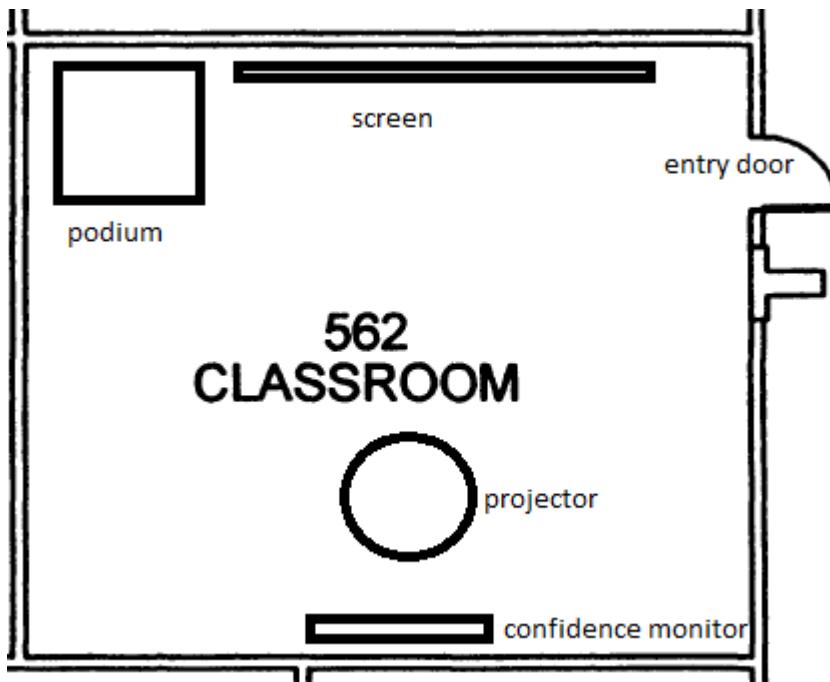

Upgrade components:

KI podium
A/V rack
HP AIO
TCL pro 720 touch panel
Projector Screen
Ceiling speakers
Blu-ray
Microphone/ assisted listening
Doc cam
Confidence monitor

Notes:

Projector Replaced

Room Availability:

M-Th 10:30AM-5:30PM End 8/4/2016


Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 563A, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Junior**

Room Layout (from room inventory document)

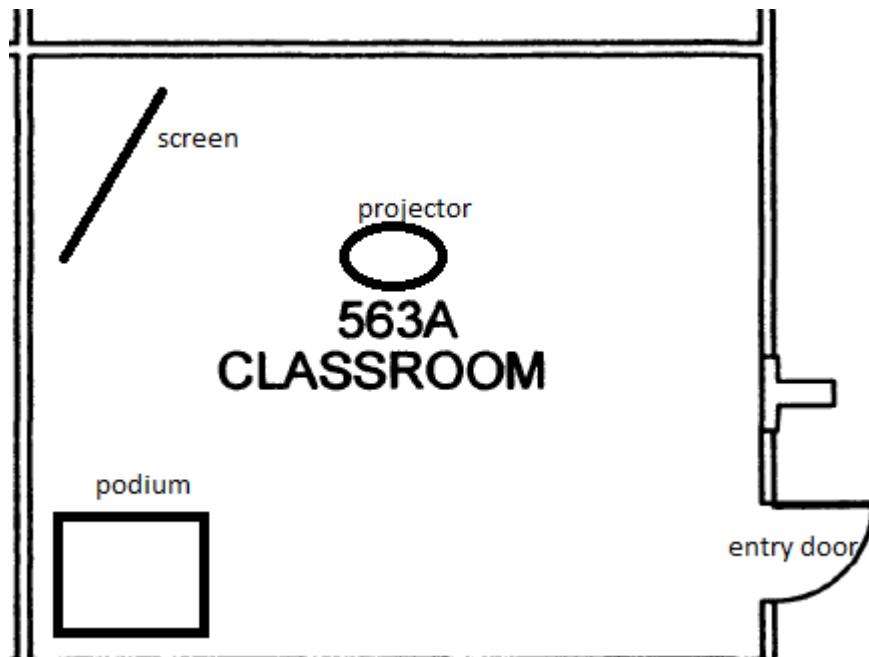

Upgrade components:

KI podium
A/V rack
HP AIO
TCL pro 720 touch panel
Casio projector
Projector Screen
Ceiling speakers
Blu-ray
Microphone/ assisted listening
Doc cam

Notes:

Room Availability:

M-Th 12PM-1:50PM

End 7/28/2016


Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 652, Office of Instruction

Project Coordinator: **Hector Reyes**

Instructional Lab Technician: **TBD**

Room Layout (from room inventory document)

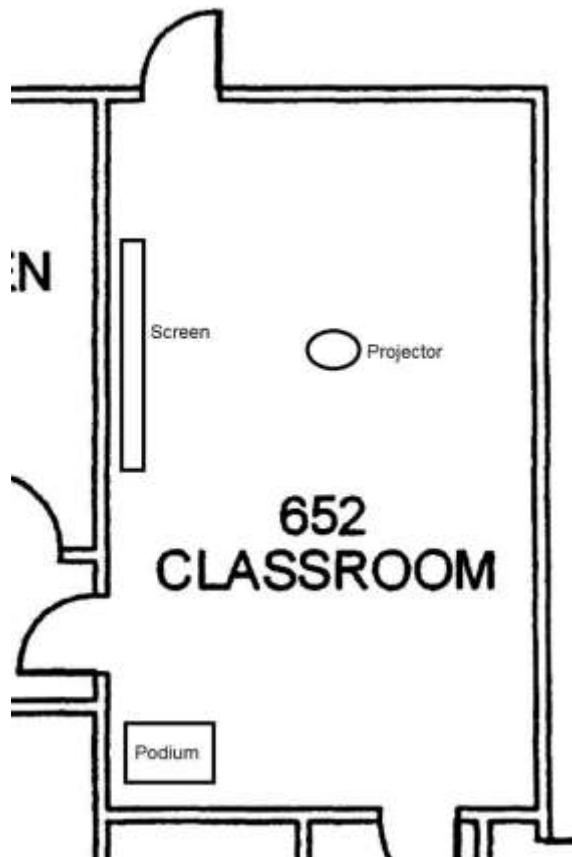

Upgrade components:

Use existing podium retro -fit

A/V rack

HP mini

TLP PRO 520M

Cable Cubby 1200

Projector Screen

Ceiling speakers

Blu-ray

Microphone/ assisted listening

Doc cam

Confidence monitor (TBD)

Notes:

Room Availability:

Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Appendix I: Task Order 1- AV Room Scope


RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 564B, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Junior**

Room Layout (from room inventory document)

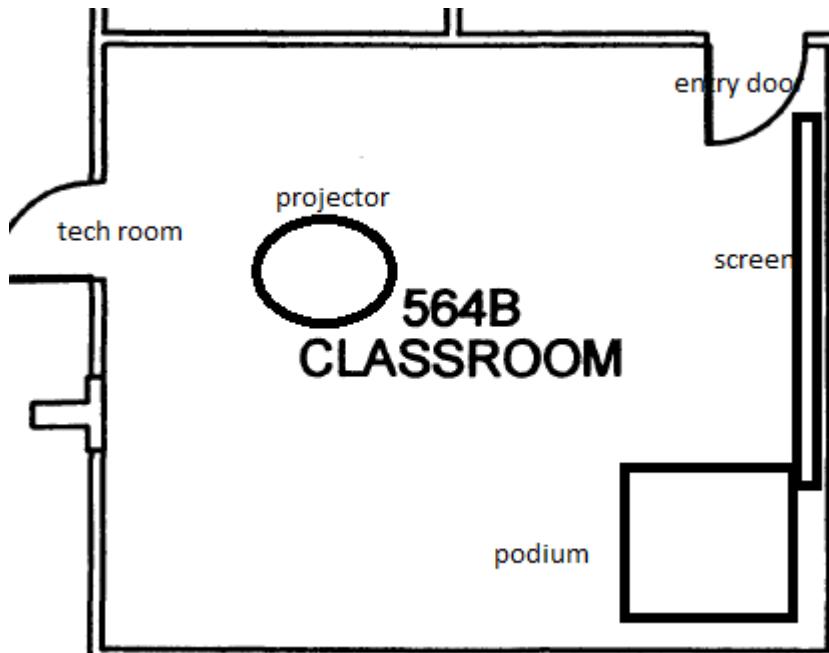

Upgrade components:

KI podium
A/V rack
HP AIO
TCL pro 720 touch panel
Projector Screen
Ceiling speakers
Blu-ray
Microphone/ assisted listening
Doc cam

Notes:

Projector Replaced

Room Availability:

M-Th 10:30AM-2:20PM End 8/4/2016

Appendix I: Task Order 1- AV Room Scope

RFP No. 1617 -151 Professional Audio-Visual Design,


Integration/Implementation Services

Room 705, Language Arts & Literature

Project Coordinator: **Barry Thele**

Instructional Lab Technician: **Marco**

Room Layout (from room inventory document)

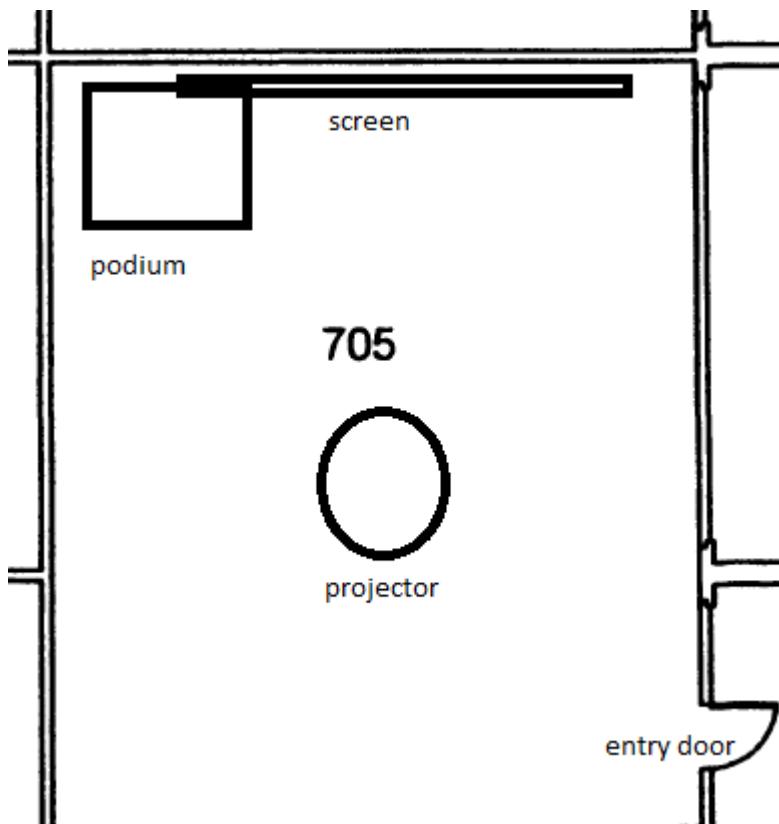

Upgrade components:

KI podium
A/V rack
HP AIO
TCL pro 720 touch panel
Projector Screen
Ceiling speakers
Blu-ray
Microphone/ assisted listening
Doc cam

Notes:

Projector Replaced

Room Availability:

M-Th 8AM-2:20PM

End 7/21/2016

Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Appendix I: Task Order 1- AV Room Scope


RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 4500, Otay Mesa

Project Coordinator: **Hector Reyes**

Instructional Lab Technician: **Nora**

Room Layout (from room inventory document)

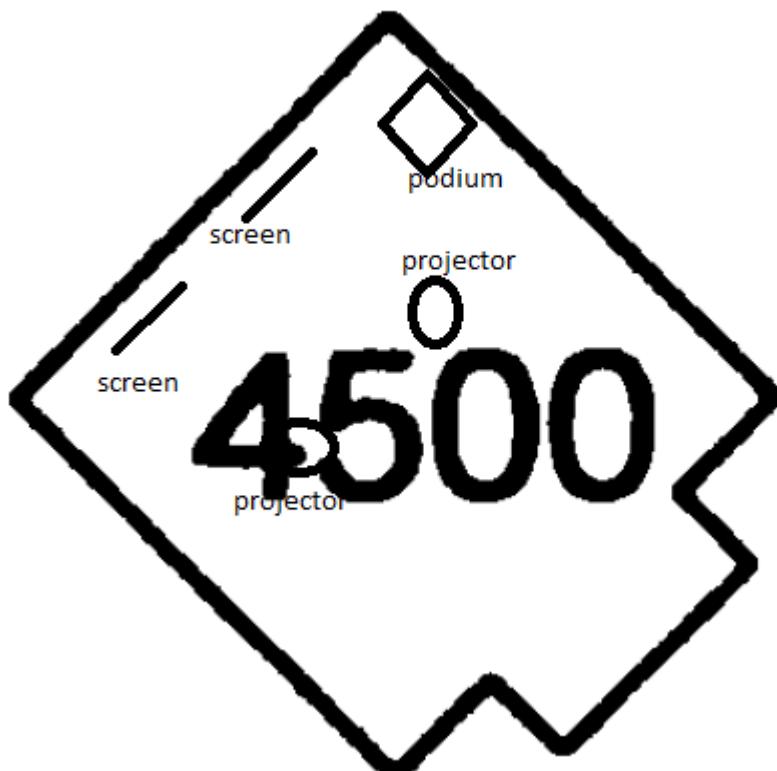

Upgrade components:

KI podium

A/V rack

HP AIO

TCL pro 720 touch panel

Panasonic projector - times two

Projector Screen - times two

Ceiling speakers times two

Blu-ray

Notes: dual projectors with large screens

Room Availability:

July 5-7 and August 1-4

Appendix I: Task Order 1- AV Room Scope

RFP No. 1617 -151 Professional Audio-Visual Design,


Integration/Implementation Services

Room 7120, National City Library

Project Coordinator: **Hector Reyes**

Instructional Lab Technician: **Marcelo Arman**

Room Layout (from room inventory document)

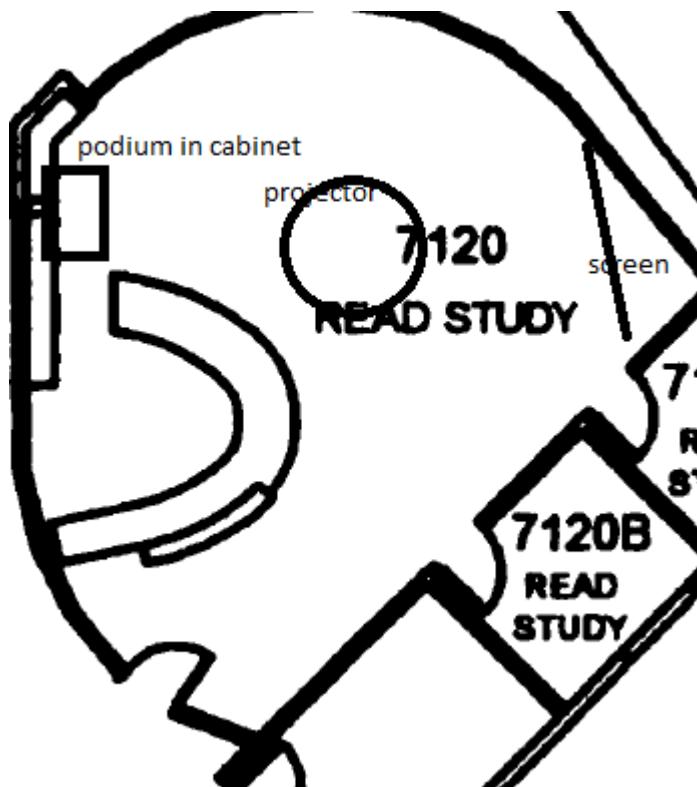

Upgrade components:

retro-fit cabinet

A/V rack

HP Mini

TLP PRO 520M

Projector Screen

Ceiling speakers

Blu-ray

Notes:

Projector Replaced

Room Availability:

Available all summer

Appendix I: Task Order 1- AV Room Scope

RFP No. 1617 -151 Professional Audio-Visual Design,


Integration/Implementation Services

Room 7202, National City

Project Coordinator: **Hector Reyes**

Instructional Lab Technician: **Marcelo Arman**

Room Layout (from room inventory document)

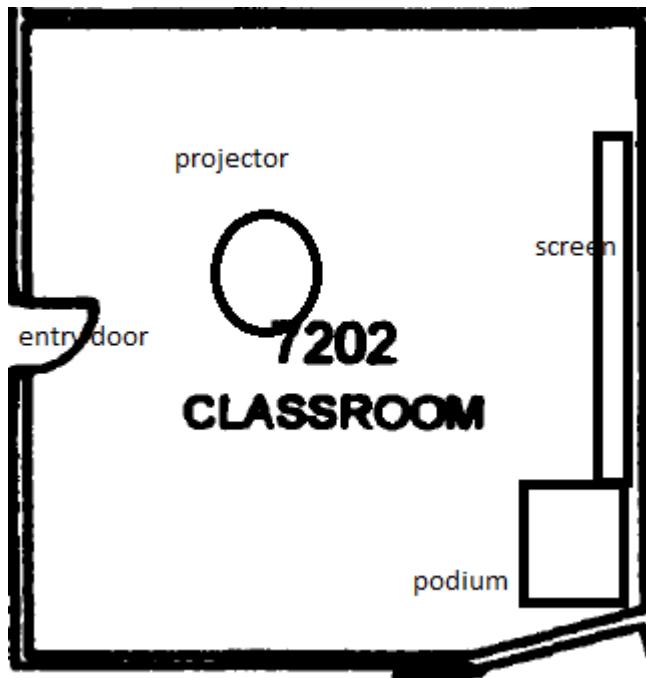

Upgrade components:

Use existing podium retro-fit

A/V rack

HP Mini

TLP PRO 520M

Cable Cubby 1200

Projector Screen

Ceiling speakers

Blu-ray

Notes:

Projector Replaced

Room Availability:

M-Th 8AM-9PM

End 8/4/2016


Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 7203, National City

Project Coordinator: **Hector Reyes**

Instructional Lab Technician: **Marcelo Arman**

Room Layout (from room inventory document)

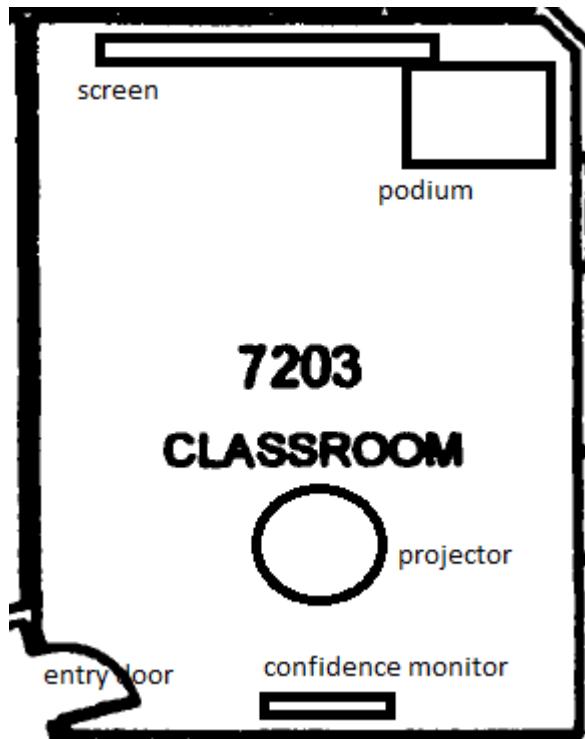

Upgrade components:

Use existing podium retro-fit

A/V rack

HP Mini

TLP PRO 520M

Cable Cubby 1200

Projector Screen

Ceiling speakers

Blu-ray

Microphone/ assisted listening

Doc cam

Confidence monitor

Notes:

Projector Replaced

Room Availability:

M-Th 7AM-2PM

End 8/4/2016

Appendix I: Task Order 1- AV Room Scope


RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 7205, National City

Project Coordinator: **Hector Reyes**

Instructional Lab Technician: **Marcelo Arman**

Room Layout (from room inventory document)

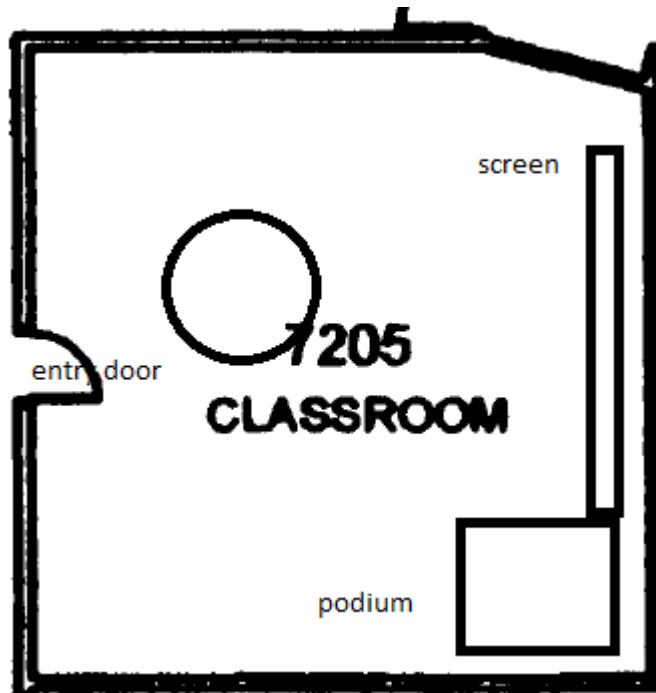

Upgrade components:

Use existing podium retro -fit

A/V rack

HP Mini

TLP PRO 520M

Cable Cubby 1200

Projector Screen

Ceiling speakers

Blu-ray

Notes:

Projector Replaced

Room Availability:

M-Th 7AM-7PM


End 8/4/2016

Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 7206, National City

Project Coordinator: **Hector Reyes**

Instructional Lab Technician: **Marcelo Arman**

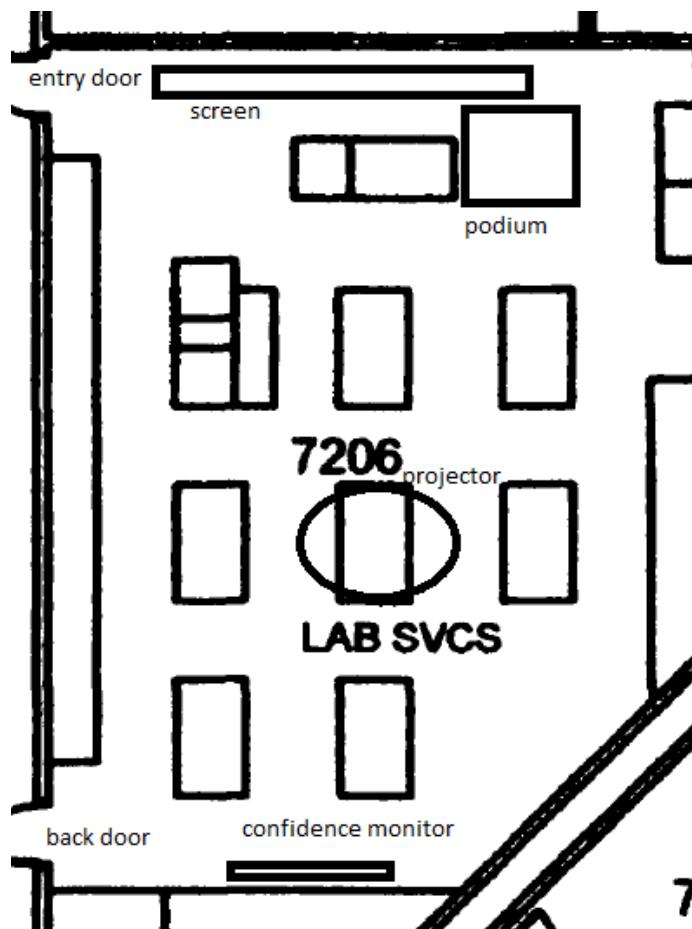

Use existing podium retro-fit

A/V rack

HP Mini

TLP PRO 520M

Cable Cubby 1200

Projector Screen

Ceiling speakers

Blu-ray -- Doc cam

Microphone/ assisted listening

Confidence monitor

Notes:

Projector Replaced

Room Availability: M-Th 8AM – 9PM End 8-4-2016

Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Appendix I: Task Order 1- AV Room Scope

RFP No. 1617 -151 Professional Audio-Visual Design,


Integration/Implementation Services

Room 7208A, National City

Project Coordinator: **Hector Reyes**

Instructional Lab Technician: **Marcelo Arman**

Room Layout (from room inventory document)

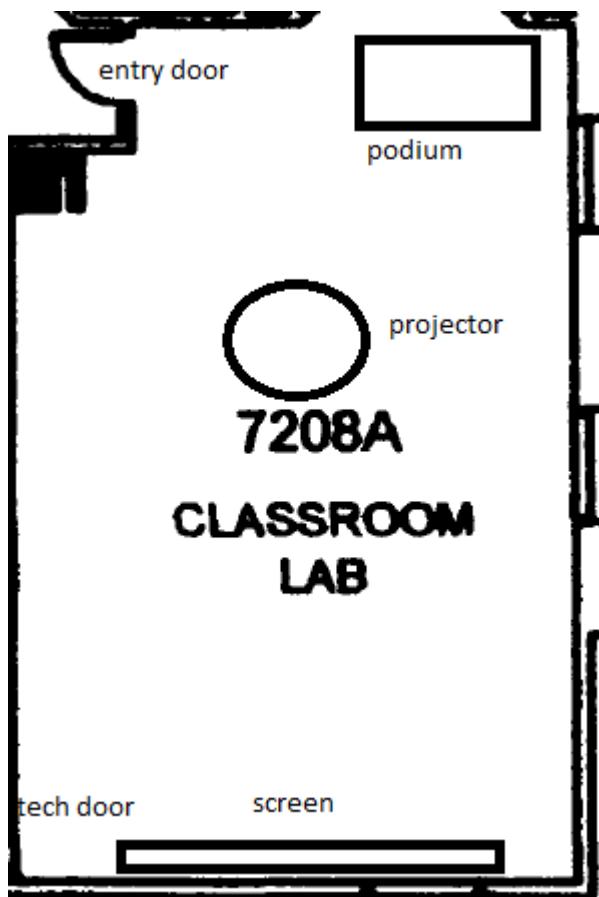

Upgrade components:

Use existing podium retro -fit

A/V rack

HP Mini

TLP PRO 520M

Casio projector

Projector Screen

Ceiling speakers

Blu-ray

Notes: this room has a matrix switcher combined between 7208A & 7208B. We are not sure if they want to put in podiums. Right now they are controlled by matrix and a digital touch panel.

Room Availability: open lab – probably available as needed for short time slots


Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 7208B, National City

Project Coordinator: **Hector Reyes**

Instructional Lab Technician: **Marcelo Arman**

Room Layout (from room inventory document)

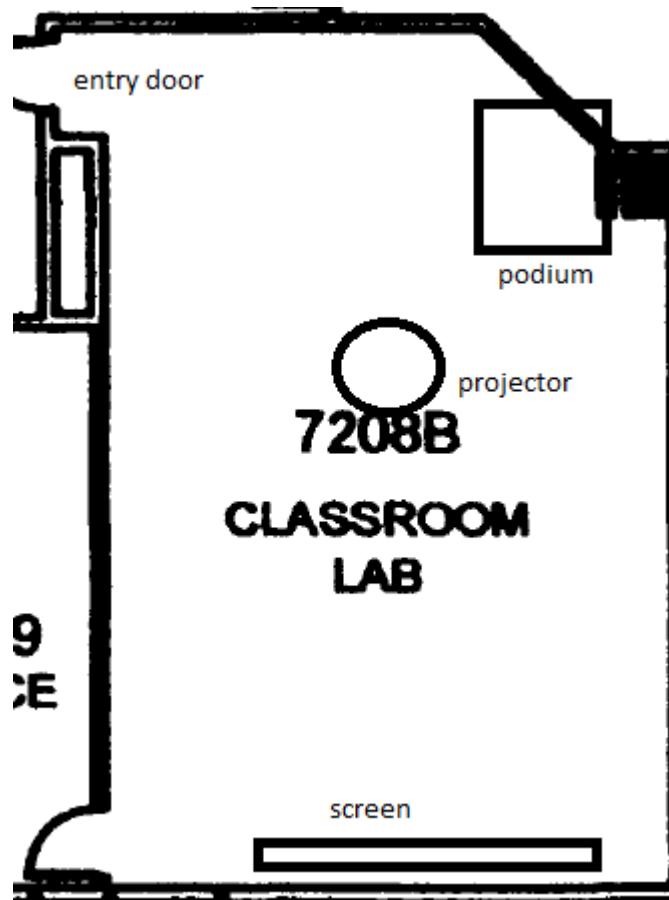

Upgrade components:

Use existing podium retro-fit

A/V rack

HP Mini

TLP PRO 520M

Cable Cubby 1200

Casio projector

Projector Screen

Ceiling speakers

Blu-ray

Notes: this room has a matrix switcher combined between 7208A & 7208B. We are not sure if they want to put in podiums. Right now they are controlled by matrix and a digital touch panel.

Room Availability:

M-W 8AM-9PM

End 7/21/2016

Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services


Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 7210, National City

Project Coordinator: **Hector Reyes**

Instructional Lab Technician: **Marcelo Arman**

Room Layout (from room inventory document)

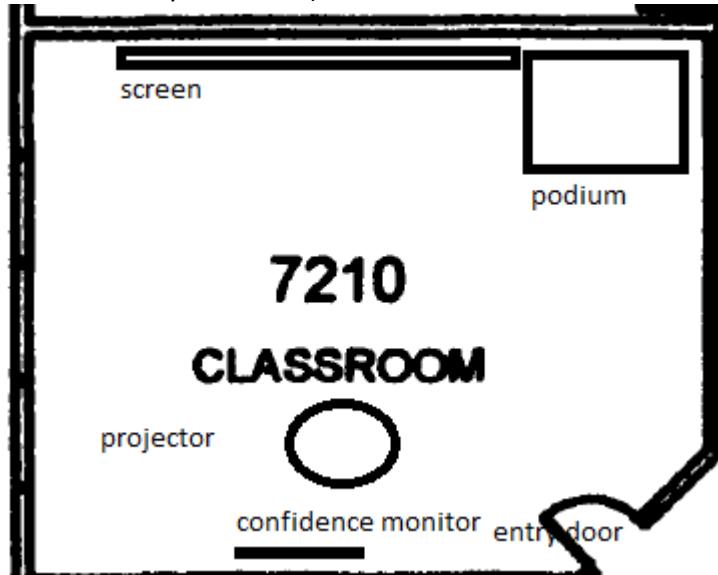

Upgrade components:

Use existing podium retro -fit

A/V rack

HP Mini

TLP PRO 520M

Cable Cubby 1200

Projector Screen

Ceiling speakers

Blu-ray

Microphone/ assisted listening

Doc cam

Confidence monitor

Notes:

Projector Replaced

Room Availability:

M-Th 7AM-9:30PM

End 8/4/2016


Appendix I: Task Order 1- AV Room Scope
RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 7211, National City

Project Coordinator: **Hector Reyes**

Instructional Lab Technician: **Marcelo Arman**

Room Layout (from room inventory document)

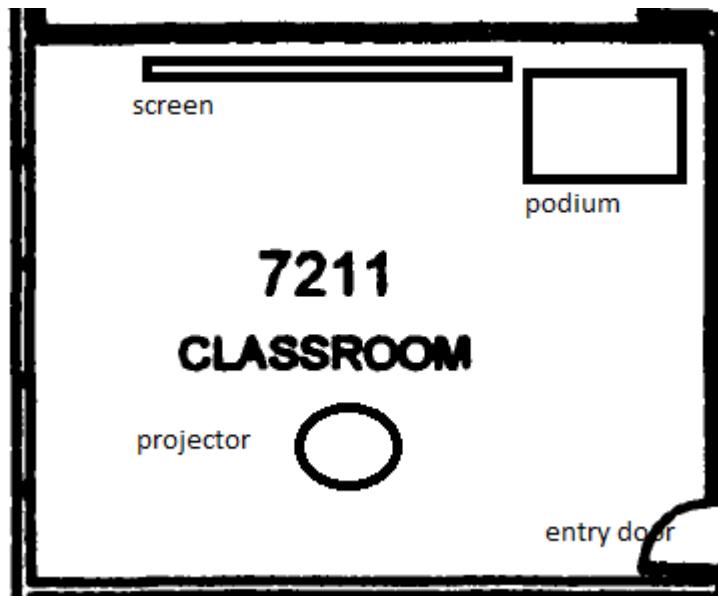

Upgrade components:

Use existing podium retro -fit

A/V rack

HP Mini

TLP PRO 520M

Cable Cubby 1200

Projector Screen

Ceiling speakers

Blu-ray

Notes:

Projector Replaced

Room Availability:

M-Th 8AM-9PM End 8/4/2016

Appendix I: Task Order 1- AV Room Scope


RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 7212, National City

Project Coordinator: **Hector Reyes**

Instructional Lab Technician: **Marcelo Arman**

Room Layout (from room inventory document)

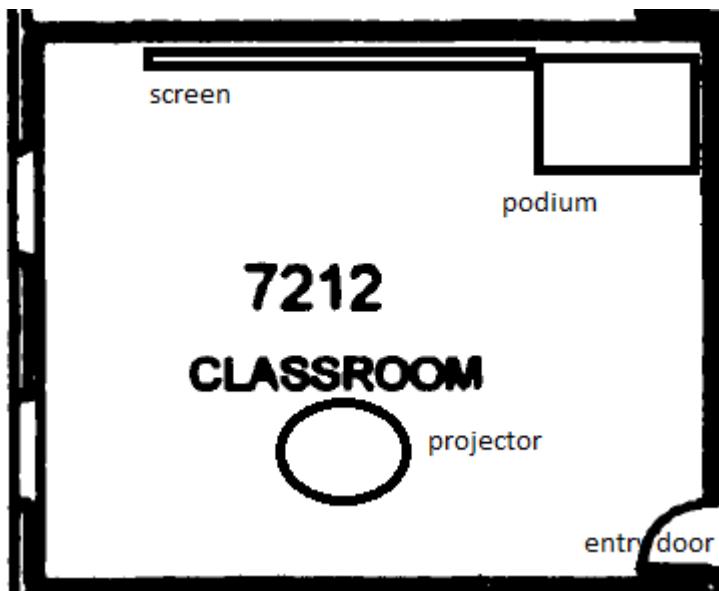

Upgrade components:

Use existing podium retro -fit

A/V rack

HP Mini

TLP PRO 520M

Cable Cubby 1200

Projector Screen

Ceiling speakers

Blu-ray

Notes:

Projector Replaced

Room Availability:

M-Th 7AM-8:30PM

End 8/4/2016

Appendix I: Task Order 1- AV Room Scope


RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 7213, National City

Project Coordinator: **Hector Reyes**

Instructional Lab Technician: **Marcelo Arman**

Room Layout (from room inventory document)

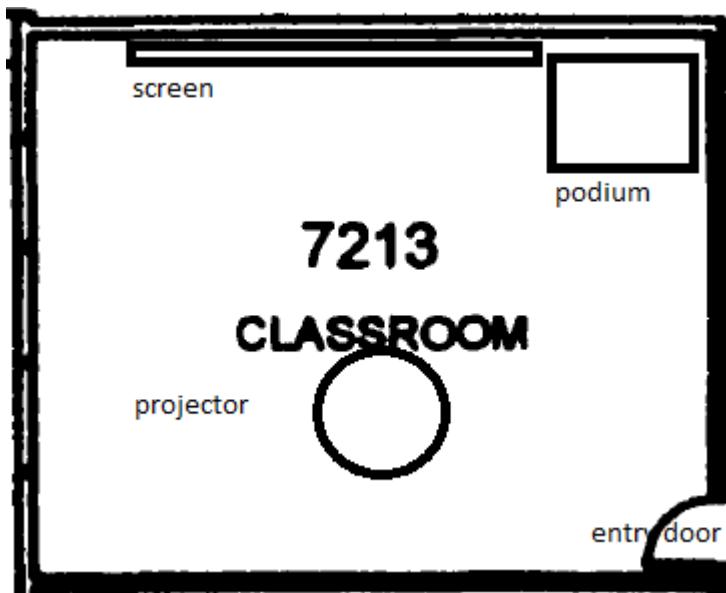

Upgrade components:

Use existing podium retro -fit

A/V rack

HP Mini

TLP PRO 520M

Cable Cubby 1200

Projector Screen

Ceiling speakers

Blu-ray

Notes:

Projector Replaced

Room Availability:

M-Th 7AM-12PM

End 8/4/2016

Appendix I: Task Order 1- AV Room Scope


RFP No. 1617 -151 Professional Audio-Visual Design,
Integration/Implementation Services

Room 7214, National City

Project Coordinator: **Hector Reyes**

Instructional Lab Technician: **Marcelo Arman**

Room Layout (from room inventory document)

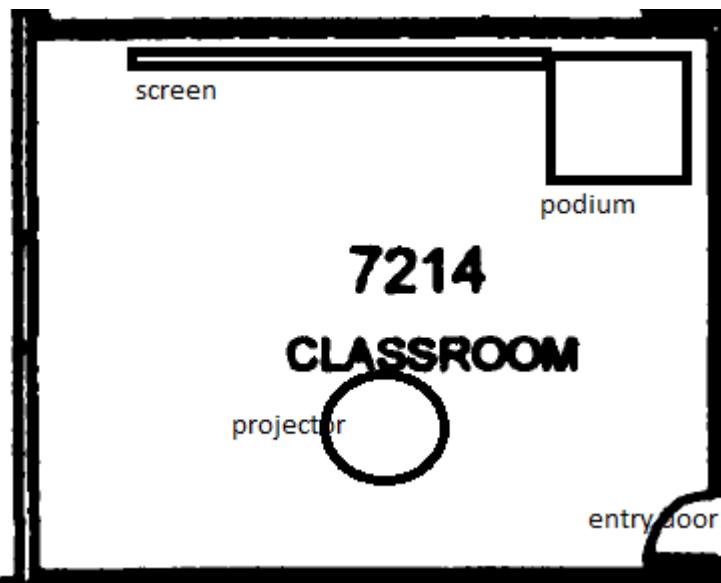

Upgrade components:

Use existing podium retro -fit

A/V rack

HP Mini

TLP PRO 520M

Cable Cubby 1200

Projector Screen

Ceiling speakers

Blu-ray

Notes:

Projector Replaced

Room Availability:

M-Th 7AM-11:30PM

End 7/21/2016

Appendix I: Task Order 1- AV Room Scope

RFP No. 1617 -151 Professional Audio-Visual Design,


Integration/Implementation Services

Room 7215, National City

Project Coordinator: **Hector Reyes**

Instructional Lab Technician: **Marcelo Arman**

Room Layout (from room inventory document)

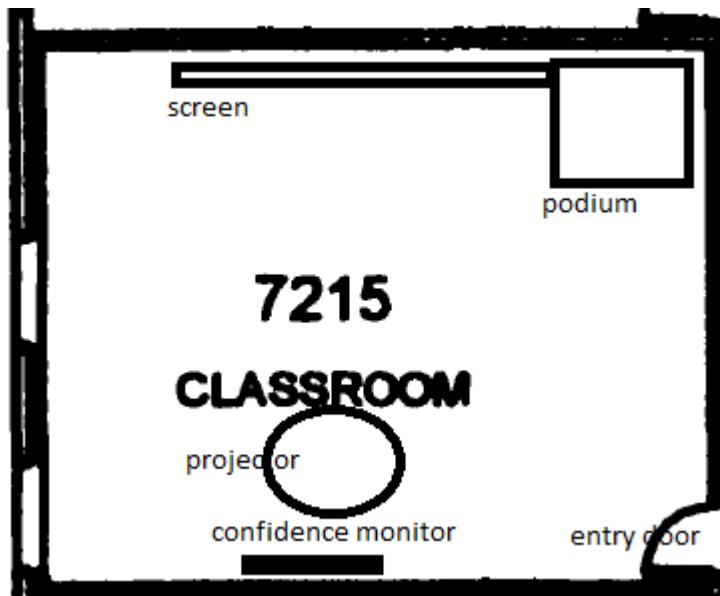

Upgrade components:

Use existing podium retro -fit

A/V rack

HP Mini

TLP PRO 520M

Cable Cubby 1200

Projector Screen

Ceiling speakers

Blu-ray

Microphone/ assisted listening

Doc cam

Confidence monitor

Notes:

Projector Replaced

Room Availability:

M-Th 7AM -11:30PM

End 7/21/2016

Appendix I: Task Order 1- AV Room Scope

RFP No. 1617 -151 Professional Audio-Visual Design,


Integration/Implementation Services

Room 7216, National City

Project Coordinator: **Hector Reyes**

Instructional Lab Technician: **Marcelo Arman**

Room Layout (from room inventory document)

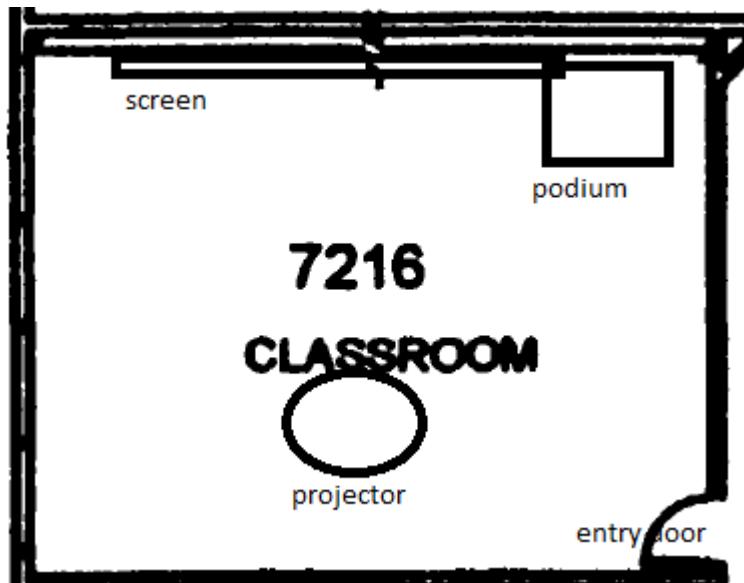

Upgrade components:

Use existing podium retro -fit

A/V rack

HP Mini

TLP PRO 520M

Cable Cubby 1200

Projector Screen

Ceiling speakers

Blu-ray

Notes:

Projector Replaced

Room Availability:

M-Th 7AM-3:30PM

End 8/4/2016
